Rural Water Supply and Sanitation Project in Western Nepal Phase II

www.rwsspwn.org.np

2018

SEMI-ANNUAL PROGRESS REPORT FY05

2074/75 – CY2017/18 (16.7.2017-14.1.2018)

Rural Water Supply and Sanitation Project in Western Nepal Phase II (09/2013-09/2019)

Ministry for Foreign Affairs of Finland

FCG

SUMMARY

This is the RWSSP-WN Phase II Semi-Annual Progress Report for the first half of the fifth Fiscal Year (FY05). It covers the six-month period of Nepali FY 2074/075 (July 16, 2017 to January 14, 2018). It presents the progress of both the programmes funded through the Municipality WASH Units (M-WASH Units) and the Municipality WASH Funds (MWFs), and the work funded through TA accounts. This report presents a brief assessment of the *impact level* progress, contextual changes, assumptions and risks as the reporting period was strongly affected by changes in the Nepalese governance system.

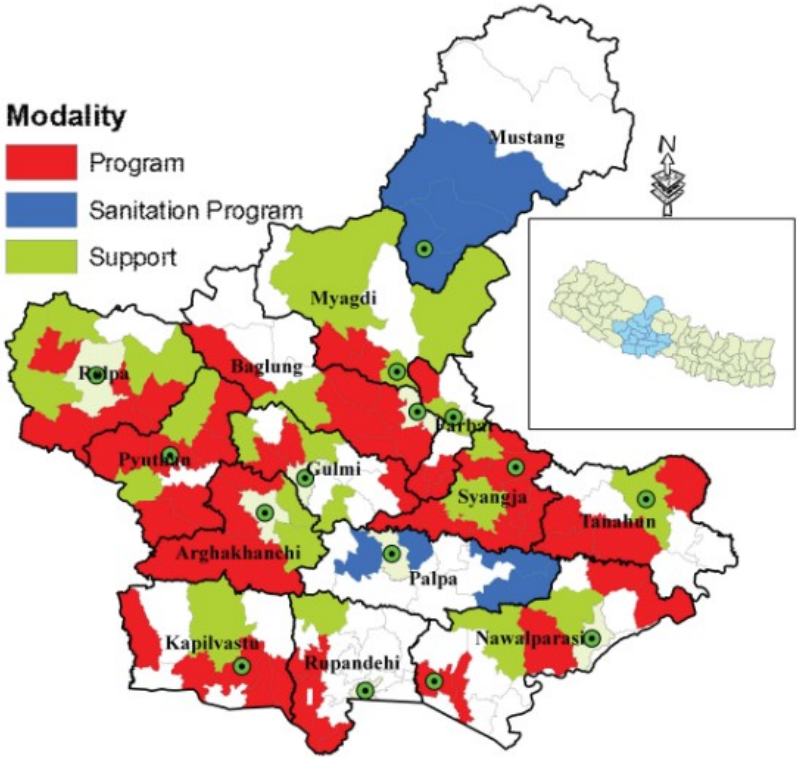

Figure 1. Project working area

Rural Water Supply and Sanitation Project in Western Nepal Phase II (RWSSP-WN II)

Project duration: 09/2013-09/2019

Project stakeholders:

- Ministry for Foreign Affairs, Government of Finland (GoF)
- Ministry of Finance, Government of Nepal (GoN)
- Ministry of Federal Affairs and Local Development (MoFALD)
- Department of Local Infrastructure Development and Agricultural Roads (DoLIDAR)
- Municipalities (both *Gaunpalikas* and *Nagarpalikas)*
- Technical Assistance (TA) consultant: FCG International (Finnish Consulting Group Ltd.) www.fcg.fi

Implementation: Municipality WASH Units & Municipality WASH Funds

Report type: Semi-Annual Progress Report

Prepared by: Project Support Unit (PSU)

Submitted: January 31, 2018

Report distribution: Public

OVERALL OBJECTIVE:

RWSSP-WN II works for improved health and fulfilment of the equal right to water and sanitation for the inhabitants of the project area through a decentralized governance system.

THREE RESULT AREAS:

Result 1. Access to sanitation & hygiene for all achieved and sustained in the project working municipalities

Result 2. Access to safe, functional & inclusive water supply services for all achieved and sustained in the project working municipalities

Result 3. Strengthened institutional capacity of government bodies to plan, coordinate, support and monitor the Water Users and Sanitation Committees and other community groups in the implementation, operation and maintenance of domestic water, sanitation and hygiene programmes in a self-sustainable manner

WORKING AREAS:

Western Development Region: Arghakhanchi, Baglung, Gulmi, Kapilvastu, Mustang, Myagdi, Nawalparasi, Palpa, Parbat, Rupandehi, Syangja & Tanahun

Mid-Western Development Region: Pyuthan and Rolpa

Province 4: Nawalparasi East, Baglung East, Mustang, Myagdi, Parbat, Syangja, and Tanahun.

Province 5: Arghakhanchi, Baglung West, Gulmi, Palpa, Kapilvastu, Rupandehi, Nawalparasi West, Pyuthan, and Rolpa.

IMPACT LEVEL PROGRESS ANALYSIS

The **Annex 1** to this report shows the detailed outcome and output level progress figures, including both semi-annual and cumulative progress since the beginning of the Phase II. **Annex 2** shows the municipality-specific progress, and **Annex 3** lists the capacity building events held during the reporting period. Despite of the difficult operational environment within the reporting period, the Project reached most of its targets and is well on track. The following five pages analyze changes, assumptions and risks through the RWSSP-WN II impact level indicators:

- Incidence of diarrhoea in under-5 children and under 5 child mortality reduced
- Incidence of water and sanitation related diseases reduced
- Improved local governance capacity to provide effective WASH service delivery
- Decreasing disparity between the worst- and best-served municipalities with regards to sanitation and water supply coverage

OVERALL OBJECTIVE: IMPROVED HEALTH

This analysis compares Nepal Demographic Health Survey data from 2011 and 2016 in the RWSSP-WN II working area. The incidence of diarrhoea is directly connected to both water supply and sanitation, also acknowledged in this report: "*The percentage of children under age 5 with diarrhoea varies according to the availability of toilet facilities"* (Ministry of Health, 2016). The percentage for diarrhoea in under five children decreased from 15.7 % (2011) to 5.3 % (2016) in Western Development Region (WDR) and from 14.6 % (2011) to 8.4 % (2016) in the Mid-Western Development Region (MWDR) between 2011 and 2016. More specifically, the Province number 4 had the lowest percentage of under five diarrhoea in all Nepal in 2016 (3.7%). However, the working Province number 5 had the third highest prevalence of diarrhoea of all provinces (8.2%).

The under 5 mortality had decreased from 57 (2011) to 39 (2016) deaths per 1,000 births in WDR and from 73 (2011) to 50 (2016) deaths per 1,000 births in MWDR. More specifically, there were 27 deaths per 1,000 births in Province 4 in 2016 and 45 deaths per 1,000 births in Province 5 in 2016. Based on the statistics, especially RWSSP-WN II working area in Province 4 (Baglung East, Mustang, Myagdi, Parbat, Syangja, Tanahun, Nawalparasi East) stands out with less under 5 diarrhoea and less under 5 mortality than any other Province in Nepal. Province 5 stands behind but has improved considerably as well in the last 5 years period.

National Climate Change Impact Survey 2016 studied the increase of the incidence of water borne disease in Nepal during the last 25 years. Western Hill area stands out positively also in the incidence of disease as only 3.52 % of the households reported increase in the area. After Western Mountain area (0 % increase), it has the top record in the whole Nepal (20.67 % in average). However, Western Terai and Mid-Western Hill have witnessed increase in waterborne disease by 34.35 % and 43.77% respectively.

Based on the statistics, especially RWSSP-WN II working area in Province 4 (Baglung East, Mustang, Myagdi, Parbat, Syangja, Tanahun, Nawalparasi East) stands out with less under 5 diarrhoea, less under 5 mortality and less waterborne disease than other areas in Nepal.

Sources: Ministry of Health and Population: Nepal Demographic and Health Survey 2011 and Nepal Demographic and Health Survey 2016

National Planning Commission Secretariat, Central Bureau of Statistics: National Climate Change Impact Survey 2016

OBJECTIVE: FULFILLMENT OF THE EQUAL RIGHT TO WATER AND SANITATION THROUGH A DECENTRALIZED GOVERNANCE SYSTEM

RWSSP-WN II faced remarkable changes in its operational environment in the first half of FY05. A new federal structure was established in Nepal with 246 municipalities and 481 rural municipalities. Nepal organized municipality level elections in May 14 and June 28, and provincial and parlamentary elections in November 26 and December 7, 2017. The changes affected RWSSP-WN II strongly as the project was deeply embedded in the former local governance units: District Development Committees and Village Development Committees. I

n the new setting, RWSSP-WN II operates in **98 local body units** of which *55 Program municipalities* (full program), *7 Sanitation program municipalities* (sanitation program only), *23 Support municipalities* (schemes only) and *13 District Coordination Committees/Technical Support Units*. FY05 started by signing the Memorandum of Understandings (MoUs) between the new municipalities and DoLIDAR (25/07/2017-29/10/2017). MoUs define the new roles and responsibilities, replacing the earlier District WASH Units with the M-WASH Units. All are available at our web-site in both English and Nepali. The Project was received well by the newly elected representatives as in all cases no-one else had signed this type of agreement with them.

While MoUs were signed within the first months of the FY, there were delays. The election code of conduct banned recruitment and gatherings. Therefore, many newly established M-WASH Units could not start the recruitment and consequently still lack staff at the end of the reporting period. There is both high turnover and non-availability of competent staff in the municipalities. The new municipalities also lack proper working environment, including desks, computers and phones. Some municipalities have faced delays in receiving funds from the central level. The Figure 2 shows the situation in the 55 Program municipality M-WASH Units as per 15/01/2018. Still after six months, one fourth of M-WASH Units lack the WASH Coordinator, more than one third lack basic facilities, almost half lack computer and one third of the WASH Coordinators need capacity building in computer skills

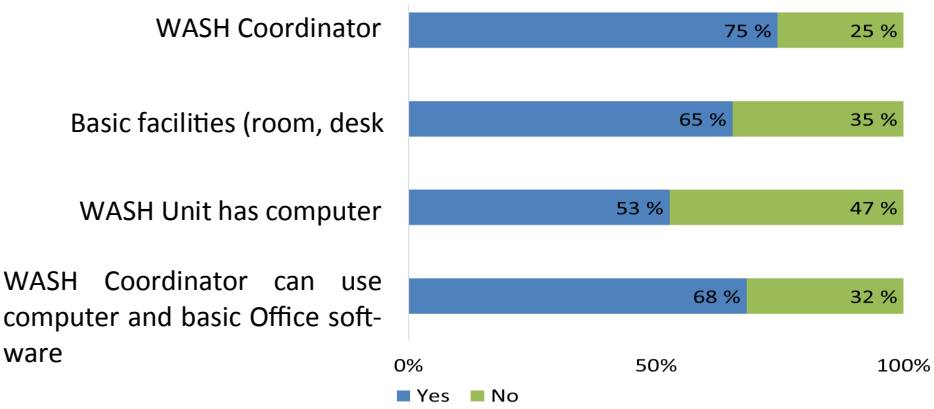

Figure 2. M-WASH Unit situation 15/01/2018. M-WASH Units n=55, WASH Coordinators n=41

Municipalities are now governed by democratically elected bodies. This increases the citizens' equal opportunities to influence the decision-making and local development. The reform can potentially improve the local governance capacity to provide effective WASH services and to decrease the disparity between the worst- and best-served municipalities.

RWSSP-WN II is implemented through local institutions to strengthen their capacities in providing sustainable WASH services. The Project is now implemented by the M-WASH Units, led by municipality-hired WASH Coordinator. These operate under the **Municipality WASH Management Committees** under the leadership of the elected Municipality Chairman. The roles and responsibilities are defined in the Memorandums of Understanding, all available at the project web-site in both English and Nepali.

Water Users and Sanitation Committees continue to have the leading role in individual water or sanitation scheme planning, implementation, procurement and later, operation and maintenance.

Since the working modality has changed, **a new indicator was introduced at the start of this FY**:

Indicator 3.7: Number of local administrative units (M-WASH Units) with established and operational policies and procedures for participation of local communities in water and sanitation management.

Considered operational if the Municipality WASH Unit can plan, implement and report their WASH Programme, verified by:

a) Municipality WASH Unit Monthly Progress Report

b) Municipality WASH Unit Monthly Workplans and staff monthly time sheets

c) Municipality WASH Unit Financial Statement from the Municipality Accounts Section

d) Municipality WASH Unit Event Report which shows the GESI aspect of participation

SUSTAINABLE SANITATION

Most of the Project working districts have declared ODF. Now the focus has turned to the sustainability of these achievements.

The Project has conducted a large-scale study on *toilet use* in ODF-declared areas of five districts Baglung, Gulmi, Parbat, Rupandehi and Syangja. As of 04/01/2018, the sample included 515 respondents.

Out of these, 44% replied that they have never done open defecation over the past 7 days. This means that more than half (56%) are still practicing open defecation.

One of the questions asked was whether there are specific days when the respondent or his/her family members do not use the toilet. Total 124 (24%) replied that yes, they or their family members do not use the toilet during menstruation.

Out of these 124, there were 42 respondents that even if they responded having not done open defecation over the past seven days, they (or their family member) would still do Open Defecation during menstruation.

This increases the number of those who would not use the toilets from 56% to 64%. This is a significant findings considering the large sample size and hinders dramatically the sustainability of the ODF movement.

Based on findings, RWSSP-WN II has paid more attention on women's toilet use during menstruation and the menstruation hygiene management *(see last page).*

RISKS, ASSUMPTIONS AND SUSTAINABILITY

Several historical events took place within the reporting period, and the Project has worked hard to align and adjust to these changes. At the moment, the main issues identified as impact level risks are:

- GoN policy changes and unclear governance system
- Absence and competence of the municipality staff
- Fragile state and security

The large number of recent policy changes have raised instability: the changes have taken place fast and often it has not been clear with what objectives. For example, at the time of writing this report, the role of the Provincial Assembly in the Federal system is still not clear even if the elections were already held. Neither is the location and role of many Project-relevant central level institutions such as the Department of Water Supply and Sewerage and even DoLIDAR. The Project has tried to decrease the instability by embedding itself on the municipality level governance.

The chances of achieving the overall objective of the Project depend largely on the success of establishing functional municipality WASH governance systems with operational M-WASH Units. Still, also at the municipality level, it will take time until the new institutions are well established and fully functional. As mentioned before in this report, the absence, circulation and the lack of competence of the municipality staff has been hindering the Project progress in the first half of the FY05. Now the elections are over and the assumption is that municipalities can recruit the needed staff within the next months.

It is clear now that within this FY the Project must put strong emphasis on its Results Area 3 to strengthen the institutional capacity of the newly established municipalities to plan, coordinate, support and monitor WASH activities. The first months of FY05 have shown that many municipalities struggle with basic issues from infrastructure to accounting and reporting. In the beginning of the FY, the Project launched new Human Resources Mobilization Guidelines to guide the work of the M-WASH Units and a web-based reporting system for M-WASH Unit monthly financial and physical reporting. The Project has also organized orientations and trainings to the WASH Coordinators and municipality accountants to capacitate them in reporting and computer skills. In most of the municipalities, there is a great interest and devotion to WASH from the elected authorities and the assumption is that with the Project support, the municipality WASH Units will become sustainable units of the local governance. If the municipalities get the support they need now in organizing and establishing themselves, the reform should lead to functional local units with the means and resources to provide sustainable WASH services to the citizens.

In the confusing governmental situation, Nepal shows as fragile state which can lead to security concerns. The confusion of the Province level governance—and even the location of the Province headquarters has led to district-wide strikes. It is possible that more strikes are to come before the situation is stabilized. Instability of this kind affects the Project operation when occurring in the working area. The Project is currently on its second last FY. That is why, despite of the high expectations and ambitious plans of the municipalities, the Project must start phasing out gradually. It is important that the Project can assure the completion and sustainability of any running works by the end of FY06. This principle will guide the work planning in the next months.

HUMAN RESOURCES

By the end of the reporting period, the Long Term Experts' actual FY05 person months spent are as follows, the target being 10.5 person months per each staff member (1 person month = 21 working days):

- 45% International experts (2 persons)
- 46% PSU-based experts (5 persons, including Chief Admin & Accounts)
- 52% District-based experts (8 District WASH Advisers in Technical Support Units)

Total 259 monitoring days were reported through the Time Sheets. This does not include such as meetings, supervision visits and training events, which in practice also have a monitoring dimension. There has been no Short Term Experts during the reporting period.

FINANCIAL RESOURCES

The total FY05 budget as entered by PCO into LBMIS is NPR 562,727,000 (EUR 4,893,278 with rate EUR:NPR 115). Together with the municipalities contributions, the total annual budget is over NPR 633,768,000. This is NPR *123,772,000 more budget than previous FY*. The following compares the present progress to the semi-annual progress last year:

- **RedBook: 46% of GoN+GoF budget released** (last year this time: 44%)
- **RedBook: 17% of GoN+GoF budget utilized** (last year this time: 18%)
- 32% of GoN budget released (last year this time: 29%)
- 16% of GoN budget utilized (last year this time: 15%)
- 48% of GoF budget released (last year this time: 54%)
- 19% of GoF budget utilized (last year this time: 21%)
- 21% of Municipalities budget released (last year this time districts: 22%)
- 12% of Municipalities budget utilized (last year this time districts: 2%)
- 36% of GoN+GoF+M budget released (last year this time: 43%)
- 17% of GoN+GoF+M budget utilized (last year this time: 17%)

The actual semi-annual contribution by the municipalities already now exceeds the annual actual *annual* contributions made by the districts in FY01 to FY03, and is already now 92% of the districts' actual contribution in FY04. Considering the highly challenging operational environment over the past six months, and the radical change from channelling the funds through the local units (98) instead of districts (14), and the fact that this year's budget is much higher than the previous year's, *the financial progress and also municipalities contributions can be described as* **excellent**!

Table 1 shows the GoF contributions for both MWFs and through TA accounts. The *'Cumulative FY01-FY05'* refers to the actual expenditure until December 2017 (*6 months of FY05), except for MWF where it refers to the released GoF budget (for actual, see above).

Table 1: Government of Finland contributions only (EUR)	FY05 (CY2017/18 - 2074/75)			Cumulative FY01-FY05*		Total Phase II budget
	Budget	Actual	Actual/ budget	Actual	% of total Phase II	
Total through MWFs	**1,460,122**	**838,267**	**57%**	**7,060,433**	**93%**	**7,617,672**
Technical Assistance	737,935	310,072	42%	3,536,609	71%	5,000,000
Running Costs	236,000	118,838	50%	924,773	77%	1,200,000
Capacity building & Governance	131,233	45,246	34%	507,314	86%	594,301
Evaluation & Monitoring	40,000	11,951	30%	64,751	43%	150,000
Total through TA accounts	**1,145,168**	**486,106**	**42%**	**5,033,447**	**72%**	**6,943,301**
Overall contingencies	0	0	0%	-	0%	312,000
Grand total through TA & DDF	**2,605,290**	**1,324,374**	**51%**	**12,093,880**	**81%**	**14,872,973**

MWF MONITORING

PSU & PCO conducted the following MWF monitoring during the reporting period; all reports are available from the PSU:

Baglung:
Galkot Municipality (18.12.2017)
Tarakhola Rural Municipality (19.12.2017)
Bareng Rural Municipality (21.12.2017)
Kathekhola Rural Municipality (4.12.2017)
Jaimini Municipality (26.12.2017)
Nishikhola Rural Municipality (28.12.2017)

Tanahun:
Ghiring Rural Municipality (01.01.2018)
Bhimad Municipality & Rishing Rural Municipality (02.01.2018)
Bhanu Municipality (03.01.2018)

Nawalparasi:
Bulingtar Rural Municipality (05.01.2018)
Madhyabindu Municipality (07.01.2018)

The Local-level Financial Management (LLFMI) accounting software that was launched for the municipalities by MoFALD, was not used in all account sections. Some accountants struggled to produce financial reports, even the *Phatwari*. The team recommends that the Project continues to support the accountants and the adequate use of the accounting software in the Municipalities, hence benefiting the entire municipality.

CROSS-CUTTING OBJECTIVES

Women and girls can hardly lead safe, productive and healthy lives without safe drinking water, adequate sanitation and hygiene facilities at home and in places of work and education.

Over the reporting period, the Project discovered that about one fourth of the menstruating women in RWSSP-WN II working districts do not use the toilets. This undermines the ODF status even in the Western Development Region that was not believed to be affected by the discriminative *Chhaupadi* tradition.

Surprised by the results, we had to take a stronger emphasis on the issue. That is why the Project launched a brief on **Menstruation, WASH and RWSSP-WN II Position Paper** to clarify and to guide the municipalities in including menstruation related issues in their work plan activities. The Project aims also to contribute to research and (multi)-sectorial policy dialogues by launching specific Menstrual Hygiene Management surveys and by sharing the findings with the sector.

The focus is on breaking taboos and mainstreaming menstruation related issues through small doable actions within the whole WASH framework from selecting a tap location to safe disposal of pads. For RWSSP-WN, menstruation is more than menstrual hygiene management. This is a rights question.

For more: RWSSP-WN Brief 2-2018: Menstruation, WASH and RWSSP-WN - Position Paper. http://www.rwsspwn.org.np/briefs2018

LIST OF ANNEXES:

Annex 1. Results matrix

Annex 2. Municipality programmes

Annex 3. Capacity building during the reporting period

LESSONS LEARNT, CONCLUSIONS & RECOMMENDATIONS

With regards to local governance capacity and institutional sustainability, there is a huge need to strengthen municipality-level institutions and improve their efficiencies. We acknowledge that the newly elected representatives have the core role and responsibility when identifying municipality-wide priorities. They must both represent their constituents and provide leadership. Therefore, it is of utmost importance that the Municipality WASH Management Committees, where also the elected members are represented, prepare the next annual work plan. Even if it is the final year of RWSSP-WN Phase II and a number of phase out issues need to be considered.

The Project is in a good position to strengthen the capacities at the municipality level. While working for WASH and technical issues, we can address the broader local governance environment. For instance, strengthening the capacity of the municipality accountants will benefit financial transactions in the entire municipality. Taken the urgent and intensive capacity building needs at the municipality level, the large number of M-WASH Units (55) is a real challenge. To ensure the quality and institutional sustainability of the M-WASH Units, the last year of RWSSP-WN Phase II has to reduce the number of these units. In the seven Sanitation Program municipalities, the Project suggested to implement the program through local community-based organizations in those locations. These sanitation-only districts should be phased out by the end of this FY.

Managing information is another challenge. At the moment the project is getting financial and progress reports from 55 municipalities as well as the Technical Support Units. To monitor the large number of units, the Project has developed a cloud-based (Google Drive) monthly reporting system that can be used for both planning and reporting purposes, and that can be accessed by several persons. To ensure the quality of data and reporting, the Project must institutionalize a system including routine monitoring of data and periodic in-depth assessments where one-to-one feedback can be given to the individual municipalities. This system has the potential of continued use at the municipalities also after the Project has phased out.

With regards to inequalities within a municipality, the WASH services need to continue to be targeted in an efficient manner. RWSSP-WN II has succeeded in this with the VDC WASH Plans (V-WASH Plans, see our webs-site for both VDC-wise V-WASH Plans and the related guidelines), and by selecting the schemes through the local government planning process with the 'serving the unserved'-principle guiding the final selection. These principles need to be mainstreamed into the M-WASH Units to ensure that the vulnerable groups and the remote corners of the municipality will continue to benefit from the WASH services. The V-WASH Plans are applicable in the new setting where the previous VDCs tend to be municipality Wards. Decreasing the disparity between the worst- and best-served communities within the municipality helps to decrease the disparity also between municipalities.

This new situation is both an opportunity and threat for the long-term sustainability: if the municipalities are not getting support at this critical moment when new municipality-level policies and practices are established, the momentum for building local WASH governance capacity for effective WASH service delivery can be lost. Operational municipalities that follow good governance and transparent decision making are the prerequisite for decreasing disparity and for improved health of the inhabitants of the area. It is more important than ever that the Project supports the fresh local authorities in their development to strong and sustainable service providers.

Annex 1 Logical Framework and Results-Targets

Table 1. Results targets by fiscal year as per actual for FY01—Semi-FY05, and as projected for FY05 and FY06.

The progress of the reporting period has been color coded by Green=on track, yellow = almost there, red=special attention needed

Phase II New scheme = Scheme that was included in the Annual Work Plan first time in Phase II
Phase I Carry over scheme = Scheme that was initiated in Phase I but was completed in Phase II
Phase I Improved scheme = Scheme that was initiated and completed in Phase I but required improvements in Phase II
PoCo Entry scheme = Any scheme initiated and completed before Phase II that is given only PoCo support in Phase II

IPC = Implementation phase completed and financially cleared
IPC* = Implementation phase completed but not financially cleared
PoCo = Post-Construction

		FY00 Baseline	FY01	Semi-FY02	FY02	Semi-FY03	FY03	Semi-FY04	FY04	Semi-FY05	FY05	FY06 End-line
	DWS beneficiaries[1]	0	24,666	38,542	61,616	64,270	82,971	88,181	110,806	**118,049**	140,000	150,000
	DWS PoCo beneficiaries[2]	0	No data	No data	No data	No data	50,431	61,491	128,664	**125,457[3]**	166,000	200,000
	Capacity building beneficiaries[4]	0	10,762	20,116	69,261	85,873	142,129	159,439	213,236	**231,554**	220,000	250,000

[1] Completed water supply schemes only.
[2] This target includes all the PoCo beneficiaries of Phase II New, Phase I Carry Over, Phase I Improved and PoCo Entry schemes. Target adjusted in Semi-Annual Progress report FY04.
[3] The definition of Post-Construction support was revised in the new edition of the Step-by-Step manual which affects the beneficiary figure
[4] Cumulative number of participants in capacity building events.

	Result 1	FY00 Baseline	FY01	Semi-FY02	FY02	Semi-FY03	FY03	Semi-FY04	FY04	Semi-FY05	FY05	FY06 End-line
	# of ODF beneficiaries[5]	0	2,391,477	2,585,445	3,141,666	3,355,442	3,784,178	3,882,820	4,000,890	**4,021,530**	4,120,285	4,410,739
	# direct (new) ODF beneficaries[6]									**34,640**		
1.1	**# of VDCs declared ODF**	0%	67%	71%	83%	88%	92%	94%	96%	From FY05 onwards counting ODF declared Municipality wards and direct ODF beneficiaries.		
		384	467	497	580	617	647	662	675			
New 1.1	**# of Municipality wards declared ODF**									**13%**		
										5		38
1.2	**# of public/institutional/ school toilets[7]**	0%	14%	24%	35%	38%	62%	64%	80%	**83%**	91%	100%
		0	31	52	77	84	137	141	177	**183**	200	220
1.3	**# of Wards declared for having achieved total sanitation[8]**	0%	6%	10%	13%	26%	54%	66%	108%	From FY05 onwards counting Total Sanitation declared HHs. Target for the next two years 50,000 HHs.		
		0	17	31	38	78	162	197	324			
New 1.3	**# of HHs that have achieved HH level Total Sanitation[9]**									**10%**		
										4,262	41,647	
1.4	**# of VDCs implementing post-ODF strategy**	0%	0%	0%	6%	30%	46%	70%	137%	From FY05 onwards the indicator will be reported under the Project purpose indicators.		
		0	0	0	5	27	41	63	123			

[5] Cumulative number of beneficiaries living in ODF declared areas
[6] New indicator: number of new beneficiaries living in households that have built a toilet within the reporting period
[7] Supported by the project fund in Phase II
[8] Wards within which each household complies with at least four out of five main Total Behaviour Change criteria as listed in the National Sanitation and Hygiene Master Plan
[9] New indicator: Number of households that comply with at least four out of five main Total Behaviour Change criteria as listed in the National Sanitation and Hygiene Master Plan

	Result 2	FY00 Baseline	FY01	Semi-FY02	FY02	Semi-FY03	FY03	Semi-FY04	FY04	Semi-FY05	FY05	FY06 End-line
	Cumulative number of schemes[10]	0	37	56	120	128	305	351	395	**409**		
2.1	**# Safe water[11]**	0%	0%	0%	68%	87%	68%	61%	72%	**74%**		100%
		0	0	0	81	111	207	213	283	**303**		
2.2	**Institutional capacity # of WUSCs** supported by the Project fund in the Phase I and Phase II inclusive and capacitated to provide sustainable services: a) WUSC registered and has a statute b) WUSC has O&M Plan c) Adequate water tariff collected d) VMW working e) gender and ethnic balance in WUSC	0%	0%	0%	70%	88%	69%	67%	90%	**a) 91%**		100%
					26%	34%	68%	62%	77%	**b) 85%**		
					18%	28%	72%	73%	81%	**c) 87%**		
					41%	45%	72%	70%	93%	**d) 95%**		
					39%	49%	52%	60%	78%	**e) 66% / 58 %**		
		0	No data	No data	84	113	210	236	357	**a) 372**		
					31	43	207	219	306	**b) 347**		
					21	36	220	256	321	**c) 356**		
					49	57	219	247	368	**d) 387**		
					47	63	158	211	307	**e) 270[12] / 237[13]**		

[10] Includes gravity, lift and overhead tank Phase II New, Phase I Carry Over, Phase I Improved and PoCo Entry schemes in IPC, IPC* and PoCo status.
[11] Number of water supply schemes supported by the Project fund in the Phase I and Phase II that apply a Water Safety Plan with CCA/DRR component.
[12] WUSC has gender balance (min.33 % women in Phase I schemes and min. 50 % women in Phase II schemes) and representative of all beneficiary ethnic groups
[13] WUSC has gender balance (min.33 % women in Phase I schemes and min. 50 % women in Phase II schemes) and at least one woman and one representative of disadvantaged ethnicity in a key position

	Result 2	FY00 Baseline	FY01	Semi-FY02	FY02	Semi-FY03	FY03	Semi-FY04	FY04	Semi-FY05	FY05	FY06 End-line
	Cumulative number of schemes	0	37	56	120	128	305[14]	351	395	**465[15]**		
2.3	**Improved services**: # of water supply schemes[16]	0%	100%	100%	100%	100%	14%	16%	62%	Indicator revised FY05 onwards (below)		
		0	37	56	120	128	44	55	244			
New 2.3	**Improved services:** # of water supply schemes. Scheme defined as improved and functional when: a) Improved: Piped b) Accessible: located on premises c) Reliability: Available when needed (all 12 months) d) Quality: free from microbial contamination									**a) 90%**		
										b) 96%		
										c) 88%		
										d) 78%		
										a) 417		
										b) 446		
										c) 410		
										d) 365		

[14] Before FY03, only completed Phase II New, Phase I Carry Over and Phase I improved schemes were included in the analysis (only new schemes). Since FY03 also PoCo Entry schemes have been included in the analysis.
[15]Before Semi-Annual Progress report FY05, the total figure consisted of all the gravity, lift and overhead tank Phase II New, Phase I Carry Over, Phase I Improved and PoCo Entry schemes in IPC, IPC* and PoCo status. Starting from Semi-Annual FY05 (due to the revised indicator), the figure consists of Phase II New, Phase I Carry Over, Phase I Improved and PoCo Entry schemes of all technologies in IPC, IPC* and PoCo status.
[16] Supported by the Project fund in Phase II that provide improved water supply services for previously unserved households in the programme area (previously unserved means no access to improved water supply). Scheme defined as improved and functional must fulfil the QARQ criteria: quantity=>25 liter per capita per day, accessibility = water fetching time not exceeding 15 minutes per roundtrip, reliability = 11 months or more of water per year, quality = absence of faecal coliforms

	Result 2	FY00 Baseline	FY01	Semi-FY02	FY02	Semi-FY03	FY03	Semi-FY04	FY04	Semi-FY05	FY05	FY06 End-line
	Cumulative number of schemes[17]	0	No data	No data	120	128	172	188	253	**263**		
2.4	**Reaching the unreached: # of water supply schemes**[18]	0%	0%	0%	80%	73%	70%	72%	77%	**77%**		
		0	No data	No data	96	94	120	135	195	**203**	255	260
2.5	**Institutional water supply: # of schools and institutional/public locations**[19]	0%	2%	6%	15%	17%	32%	39%	62%	**76%**	67%	100%
		0	6	18	46	51	96	117	185	**200**	200	300

[17] Number of Phase II New, Phase I Carry Over and Phase I Improved schemes in IPC, IPC* and PoCo status (all technologies)
[18] Number of schemes supported by the Project fund in the Phase II reaching the unreached (previously unserved by improved water supply supported by interventions external to municipality).
[19] Number of schools, and institutional and public locations supported by the project fund in Phase II that have safe and functional water supply with accessible water points to all users.

	Result 3	FY00 Baseline	FY01	Semi-FY02	FY02	Semi-FY03	FY03	Semi-FY04	FY04	Semi-FY05	FY05	FY06 End-line
3.1	**# of districts have D WASH Plan** that is used and periodically updated	0%	17%	42%	67%	75%	83%	83%	92%	Final target 12 districts. From FY05 onwards focus on the operation of Municipalities		
		0	2	5	8	9	10	10	11			
3.2	**# of VDCs have V WASH Plan** that is used and periodically updated	0%	0%	0%	0%	30%	79%	100%	100%	Achieved. From FY05 onwards focus on the operation of Municipalities		
		0	0	0	0	27	71	90	90			
3.3	**# of DDCs practicing coordinated** and inclusive planning through D-WASH-CC as per the D-WASH-CC Terms of Reference	0%	No data	No data	No data	No data	50%	50%	No data	Final target 12 districts. From FY05 onwards focus on the operation of Municipalities		
		0					6	6				
3.4	**# of VDCs practicing coordinated** and inclusive planning through V-WASH-CC as per the V-WASH-CC Terms of Reference.	0%	0%	0%	0%	0%	0%	33%	61%	Final target 90 VDCs. From FY05 onwards focus on the operation of Municipalities		
		0	No data	No data	No data	No data	No data	30	55			
3.5	**Annual performance evaluation** done in each district and its D-WASH Unit as per the performance indicators signed in the MOUs in between DDCs and DoLIDAR	0%	0%	0%	100%	100%	100%	100%	No data	Final target 12 districts. From FY05 onwards focus on the operation of Municipalities		
		0	0	0	10	10	12	12				

	Result 3	FY00 Baseline	FY01	Semi-FY02	FY02	Semi-FY03	FY03	Semi-FY04	FY04	Semi-FY05	FY05	FY06 End-line
3.6	**# of studies** relating to service delivery, sustainability and related mechanisms	0%	9%	19%	36%	51%	59%	76%	80%	**96%**	93%	100%
		0	6	13	25	36	41	53	56	**67**	65	70
	Number of M-WASH Units									**55**		
3.7	**# of Municipality WASH Units** with established and operational policies and procedures for participation of local communities in water and sanitation management. a) Municipality WASH Unit's Monthly Progress Report b) Municipality WASH Unit's Monthly Workplans and staff monthly time sheets c) Municipality WASH Unit Financial Statement from the Accounts Section d) Municipality WASH Unit Event Report which shows the GESI aspect of participation									**a) 95%**		100 %
										b) 51%		
										c) 69%		
										d) 89%		
										a) 52		
										b) 28		
										c) 38		
										d) 49		

RWSSP-WN II

Annex 2 Water supply schemes FY2074/2075

District	Municipality	Wards	Scheme name	Scheme Technology	Status Poush	Total HHs	Total Pop.	Estimated Total Cost (MWF+users)	Expenditure Up to Poush MWF only	GON Estimated	GOF Estimated	Municipality	Users Cash Estimated	Users Kind Estimated	Others Est.
Arghakhanchi	Bhumikasthan	4	Bhutakadula Falamkhilji lift DWS, 4	Solar Lift	PL	122	657	3,013,000	-	1,052,000	1,052,000	210,000	30,000	669,000	-
Arghakhanchi	Bhumikasthan	3	Sikhra DWS	Electrical Lift	IPO	138	801	8,000,000	3,768,000	2,760,000	2,760,000	800,000	80,000	1,600,000	-
Arghakhanchi	Bhumikasthan	10	Aarichaur Lisepani DWS, 10	Gravity	PL	84	427	3,548,500	-	982,500	981,000	350,000	35,000	1,200,000	-
Arghakhanchi	Chhatradev	2	Arbun Lift DWS	Electrical Lift	IPO	110	753	7,621,534	4,025,464	2,530,086	2,530,086	762,153	76,215	1,722,994	-
Arghakhanchi	Malarani	4	Kalaraha Jawaha Jalkanda Lift DWS	Solar Lift	PPO	150	750	14,058,000	-	5,304,000	5,304,000	1,060,000	140,000	2,250,000	-
Arghakhanchi	Malarani	5	Bhutakadula kaulemare chauradhaba ghattekhola DWS	Dropped	Dropped	0	0	-	-	-	-	-	-	-	-
Arghakhanchi	Malarani	7	Chisapani ratapani chhahara Bamruk Lift DWS	Dropped	Dropped	0	0	-	-	-	-	-	-	-	-
Arghakhanchi	Malarani	5	Chhahara Sungreni DWS	Gravity	IPO	59	331	4,168,818	1,327,726	995,098	995,098	416,882	41,688	1,720,052	-
Arghakhanchi	Malarani	6	Mihalpani Lift DWS	Electrical Lift	IPO	154	875	12,780,088	6,604,280	3,871,948	3,871,948	1,278,009	127,801	3,630,383	-
Arghakhanchi	Pandini	4	Tijukorukh Sandhagaira Lift DWS	Electrical Lift	IPO	185	919	12,699,317	3,720,000	3,466,863	3,466,863	1,269,932	126,993	4,368,666	-
Arghakhanchi	Sitganga	7	Musleghat Dhuwakhola Lift DWS, 7	Solar Lift	PPO	100	590	11,796,000	-	4,365,000	4,365,000	950,000	116,000	2,000,000	-
Arghakhanchi	Sitganga	7	Balkalyan DWS	Solar Lift	IPC*	54	336	5,169,483	1,530,000	1,552,042	1,552,042	516,950	51,695	1,496,755	-
Arghakhanchi	Sitganga	9	Dihi DWS	Gravity	IPO	39	237	4,231,832	1,771,730	1,093,285	1,093,285	423,153	80,315	1,541,794	-
Baglung	Badigad	8	Pokhara Danda	Gravity	IPC*	99	533	13,157,137	6,941,855	4,078,713	4,078,713	1,315,714	131,571	3,552,427	-
Baglung	Bareng	5	Kholakharka Kamarko puchhar DWs	Gravity	PPC	36	204	4,362,000	-	1,352,220	1,352,220	436,200	43,620	1,177,740	-
Baglung	Bareng	3	Khaltepani Rotekhola DWS	Gravity	IPO	115	690	6,941,957	1,892,092	1,753,253	1,753,253	694,196	69,420	2,671,837	-
Baglung	Bareng	3	Ligdi DWS	Gravity	IPO	57	348	7,509,402	2,322,656	2,172,468	2,172,468	750,940	75,094	2,338,432	-
Baglung	Galkot	8	Lasune Pani DWS	Gravity	IPC	78	498	3,584,127	1,588,530	883,568	883,568	358,413	35,841	1,422,738	-
Baglung	Galkot	8	Phulbari DWS	Gravity	IPO	14	91	1,949,605	701,857	604,378	604,378	194,961	19,496	526,393	-
Baglung	Galkot	8	Bhulkemul DWS	Gravity	IPO	175	1006	8,089,274	-	2,393,757	2,393,757	808,927	80,893	2,411,939	-
Baglung	Jaimini	8	Inglung DWS	Gravity	PPO	29	130	1,500,000	-	465,000	465,000	150,000	15,000	405,000	-
Baglung	Jaimini	3	Thuldanda DWS	Gravity	PPO	86	494	6,746,900	-	2,091,539	2,091,539	674,690	67,469	1,821,663	-
Baglung	Jaimini	5	Jimire Mulabari DWS	Solar Lift	PPO	72	436	8,155,785	-	2,528,293	2,528,293	815,579	81,558	2,202,062	-
Baglung	Jaimini	2	Tallo Chaurase Suntalchaur	Gravity	IPC*	41	239	2,235,940	736,027	691,308	691,308	223,594	22,359	607,371	-
Baglung	Jaimini	4	Gaw Sarkuwa DWS	Solar Lift	IPC*	101	735	5,476,782	1,807,338	1,697,802	1,697,802	547,678	54,768	1,478,731	-
Baglung	Jaimini	2	Kaldhunga solar lift DWS	Gravity	IPO	30	135	4,785,325	1,579,157	1,483,451	1,483,451	478,532	47,853	1,292,038	-
Baglung	Jaimini	2	Upallo Chairase	Gravity	IPO	130	792	5,209,142	2,474,388	1,442,310	1,442,310	520,914	48,499	1,755,108	-
Baglung	Kathekhola	2	Dunurekhola Sang khola DWS - 2	Gravity	PL	120	500	4,000,000	-	1,240,000	1,240,000	400,000	40,000	1,080,000	-

District	Municipality	Wards	Scheme name	Scheme Technology	Status Poush	Total HHs	Total Pop.	Estimated Total Cost (MWF+users)	Expenditure Up to Poush MWF only	GON Estimated	GOF Estimated	Municipality	Users Cash Estimated	Users Kind Estimated	Others Est.
Baglung	Kathekhola	2	Bhuniya Dapasa DWS	Gravity	PPC	26	178	4,878,000	-	1,512,180	1,512,180	487,800	48,780	1,317,060	-
Baglung	Nishikhola	5	Tilkhumul DWS	Gravity	IPO	66	407	4,917,450	1,396,373	1,298,025	1,298,025	491,745	49,175	1,780,481	-
Baglung	Nishikhola	5	Bahunpani DWS	Gravity	PL	287	1300	6,000,000	-	1,860,000	1,860,000	600,000	60,000	1,620,000	-
Baglung	Nishikhola	5	Majhban DWS	Gravity	PPO	16	113	1,800,000	-	558,000	558,000	180,000	18,000	486,000	-
Baglung	Nishikhola	5	Jaulepani DWS	Gravity	PPO	59	282	4,220,000	-	1,308,200	1,308,200	422,000	42,200	1,139,400	-
Baglung	Tarakhola	3	Tarima DWS	Gravity	PPO	10	68	2,527,000	-	783,370	783,370	252,700	25,270	682,290	-
Baglung	Tarakhola	1	Ashauje Bhuskat DWS	Gravity	PPO	111	679	6,575,000	-	2,038,250	2,038,250	657,500	65,750	1,775,250	-
Baglung	Tarakhola	1	Majhakharka DWS	Gravity	PPO	281	1611	10,095,000	-	3,129,450	3,129,450	1,009,500	100,950	2,725,650	-
Gulmi	Chhatrakot	4	Thumka E. Lift DWS, Digam	Electrical Lift	IPC*	166	903	12,578,719	7,547,232	4,465,446	4,465,446	1,257,871	125,787	2,264,169	-
Gulmi	Chhatrakot	3	Deuralikhola Valupani E.Lift DWS	Electrical Lift	IPO	190	951	11,344,959	5,993,079	3,749,176	3,749,176	1,134,496	113,450	2,598,661	-
Gulmi	Dhurkot	7	Machebyad Gangekholi Loft DWS	Electrical Lift	IPO	124	590	13,149,277	4,660,601	4,397,615	4,397,615	1,314,928	131,493	2,907,626	-
Gulmi	Dhurkot	3	Ghosh Bardbas E. Lift DWS	Electrical Lift	PPO	133	789	14,488,583	-	4,360,840	4,360,840	1,421,858	412,186	3,932,859	-
Gulmi	Ishma	5	Upallo Chaptari Damar Ratamata Lift DWS	Electrical Lift	IPO	81	495	9,296,724	3,457,991	3,264,309	3,264,309	581,045	188,438	1,998,622	-
Gulmi	Ishma	6	Chaurasi DWS, Ishma -6	Gravity	PPC	63	431	4,656,136	-	1,330,857	1,330,857	469,488	46,518	1,478,416	-
Gulmi	Kaligandaki	1	Bakewa DWS, Kaligandaki -1	Gravity	PPO	19	132	6,365,000	-	1,900,000	1,900,000	700,000	65,000	1,800,000	-
Gulmi	Kaligandaki	6	Rajuka Rukh Lift DWS	Gravity	IPO	96	581	4,802,752	1,363,282	1,270,227	1,270,227	480,275	48,028	1,733,994	-
Gulmi	Madane	3	Tindhare DWS	Gravity	IPO	252	1653	19,470,395	8,616,944	5,076,756	5,076,756	1,947,039	194,704	6,175,140	1,000,000
Gulmi	Mushikot	1	Chordhara Bange Lift DWS	Electrical Lift	IPO	169	887	13,928,163	5,710,548	5,014,139	5,014,139	1,392,816	139,282	2,367,787	-
Gulmi	Mushikot	2	Jalkune Saurepata Lift DWS	Electrical Lift	IPO	164	928	13,291,164	4,634,967	4,369,143	4,369,143	1,329,116	132,912	3,090,849	-
Gulmi	Mushikot	6	Bhuwachidi Beltari DWS, Mushikot -6	Gravity	PPC	190	1447	7,072,689	-	2,192,534	2,192,534	707,269	70,726	1,909,626	-
Gulmi	Mushikot	9	Thulapadhera DWS, Musikot Municipality-9	Electrical Lift	PPO	91	620	5,095,331	-	1,552,956	1,552,956	509,533	50,953	1,428,933	-
Kapilvastu	Bijayanagar	1,2	Janchetana Khanepani (Tubewell) Scheme	Tube Well	IPO	122	766	2,022,231	-	728,003	728,003	202,223	20,222	343,779	-
Kapilvastu	Kapilvastu	9,10	Niglihawa Tubewell Scheme	Tube Well	PPO	125	625	2,083,000	-	1,000,000	500,000	208,000	21,000	354,000	-
Kapilvastu	Mahrajganj	1	Khaki Baba Khanepani (Tubewell) Scheme	Tube Well	IPO	125	933	2,078,213	-	748,157	748,157	207,821	20,782	353,296	-
Myagdi	Annapurna	5	Hartukhola DWS	Gravity	IPC*	14	91	3,664,587	1,934,902	1,136,022	1,136,022	366,459	36,646	989,438	-
Myagdi	Beni NP	5	Pulachaur Daduwa WSS	Solar Lift	IPO	93	554	13,382,949	7,065,824	4,148,714	4,148,714	1,338,295	372,179	3,375,047	-
Myagdi	Dhaulagiri	7	Kotkhola III WS	Gravity	IPO	344	1903	26,788,555	7,608,391	4,219,880	4,219,880	2,678,856	903,563	8,198,459	6,567,917

District	Municipality	Wards	Scheme name	Scheme Technology	Status Poush	Total HHs	Total Pop.	Estimated Total Cost (MWF+users)	Expenditure Up to Poush MWF only	GON Estimated	GOF Estimated	Municipality	Users Cash Estimated	Users Kind Estimated	Others Est.
Myagdi	Malika	2	Thulagaira DWS	Gravity	PPO	61	401	3,226,000	-	1,286,000	714,000	323,000	32,000	871,000	-
Myagdi	Malika	4	Jukepani DWS	Gravity	IPO	69	467	5,635,017	-	2,235,975	1,257,736	563,501	56,350	1,521,455	-
Myagdi	Malika	7	Tale DWS	Gravity	IPO	25	150	2,712,861	861,336	807,079	807,079	271,286	27,129	800,289	-
Myagdi	Malika	4	Chunare DWS	Gravity	IPO	70	456	3,740,147	1,238,471	1,345,874	757,054	374,015	37,401	1,225,803	-
Myagdi	Malika	4	Chhyarchhyare Bhongsha DWS	Gravity	IPO	44	268	4,503,265	1,621,175	1,786,896	1,005,129	450,327	45,033	1,215,882	-
Myagdi	Malika	4	Dillikhola DWS	Gravity	IPO	58	345	5,373,246	-	2,132,104	1,199,309	537,325	53,732	1,450,776	-
Myagdi	Malika	4	Bandar Mul DWS	Gravity	IPO	54	323	6,515,845	-	2,585,487	1,454,337	651,585	65,158	1,759,278	-
Myagdi	Malika	2	Paa Jhikne Khola DWS	Gravity	IPO	55	317	3,670,028	-	1,327,789	746,881	367,003	36,700	1,191,655	-
Myagdi	Malika	7	Bima Lift DWS	Solar Lift	PPC	111	565	11,288,000	-	4,500,000	2,500,000	1,130,000	110,000	3,048,000	-
Myagdi	Mangala	2	Chisapani DWS	Gravity	IPO	47	316	4,750,683	-	1,862,816	1,047,834	475,068	47,507	1,317,458	-
Myagdi	Mangala	7	Bhitriban DWS	Gravity	IPO	65	375	6,522,611	2,152,461	2,022,009	2,022,009	652,261	65,226	1,761,105	-
Myagdi	Mangala	1	Panchaase Okharbot DWS	Gravity	IPO	85	454	7,331,600	2,554,687	2,800,777	1,575,437	733,160	73,316	2,148,911	-
Myagdi	Mangala	3	Bafuwa DWS	Gravity	IPO	61	417	7,669,541	2,530,949	2,377,558	2,377,558	766,954	76,695	2,070,776	-
Nawalparasi	Bulingtar	6	Besi DWS	Gravity	IPO	10	66	943,136	487,725	285,965	285,965	94,314	9,431	267,460	-
Nawalparasi	Bulingtar	6	Lapak DWS	Gravity	IPO	34	222	2,562,081	1,352,879	794,245	794,245	256,208	25,621	691,762	-
Nawalparasi	Bulingtar	6	Ghumari DWS	Gravity	IPO	41	220	1,482,850	-	459,684	459,684	148,285	14,829	400,370	-
Nawalparasi	Bulingtar	6	Kamere DWS	Gravity	IPO	35	221	1,667,571	-	456,649	456,649	166,757	16,676	570,840	-
Nawalparasi	Gaindakot	18	Hurjil DWSS	Solar Lift	IPO	45	267	1,836,632	-	618,162	618,162	238,762	18,366	343,179	-
Nawalparasi	Gaindakot	3	Hiunde DWSS	Gravity	IPO	48	354	3,951,050	-	1,124,826	1,124,826	395,105	39,511	1,066,784	200,000
Nawalparasi	Madhyabindu	12	Nayabelahani DWS	Gravity	IPO	333	1761	7,665,836	-	1,661,670	1,661,670	766,584	76,658	3,499,253	-
Nawalparasi	Ramgram	10, 16	Hakui Hand pump DWS(carriedover)	Tube Well	IPC*	110	771	1,939,300	1,156,267	683,881	683,881	193,930	25,000	352,608	-
Nawalparasi	Ramgram	10, 16	Hakui handpump WS scheme II	Tube Well	PPO	125	800	1,477,000	-	800,000	300,000	160,000	17,000	200,000	
Nawalparasi	Ramgram	12, 13	Kunwar OHT	OHT Solar	IPO	180	1113	3,685,834	3,485,834	1,680,476	1,680,476	324,882	-	-	-
Nawalparasi	Ramgram	12	Kasiya Pachgau	OHT Solar	IPO	257	1439	4,156,730	3,891,099	1,887,183	1,887,183	382,364	-	-	-
Nawalparasi	Ramgram	13	Padatikar Siwangadh	OHT Solar	IPO	183	1109	4,442,397	4,183,647	2,029,072	2,029,072	384,254	-	-	-
Nawalparasi	Sarawal	2, 3	Manari Hand Pump DWS	Tube Well	PPC	319	1734	2,484,986	-	871,111	871,111	248,499	30,000	464,265	-
Parbat	Bihadi	2	Rasauli lift DWSS, Bihadi	Dropped	Dropped	0	0	-	-	-	-	-	-	-	-
Parbat	Bihadi	3	Rumta Lift DWSS, Bihadi	Dropped	Dropped	0	0	-	-	-	-	-	-	-	-
Parbat	Bihadi	3	Lakuri DWSS, Bihadi	Dropped	Dropped	0	0	-	-	-	-	-	-	-	-
Parbat	Bihadi	2,3	Lise Gaira DWSS, Bihadi	Gravity	IPO	182	1263	14,910,751	4,810,681	4,065,143	4,065,143	1,491,075	910,000	4,379,390	-
Parbat	Bihadi	5	Majhuwa khola Bhaterpata Lift DWS	Electrical Lift	IPO	49	349	10,021,544	3,474,542	3,568,915	3,568,915	1,002,155	255,000	1,626,559	
Parbat	Bihadi	3	Ratmate Dhab Gaira DWS	Point Source Improv	IPC*	14	81	595,937	196,650	184,744	184,744	59,592	5,960	160,897	
Parbat	Jaljala	6	Sahela DWSS, Jalajala	Gravity	IPO	18	117	1,864,545	671,236	578,009	578,009	186,455	90,000	432,073	-
Parbat	Jaljala	6	Thotneri DWSS,Jalajala	Gravity	IPO	62	418	7,158,852	2,473,000	2,115,126	2,115,126	715,885	325,000	1,887,715	-

District	Municipality	Wards	Scheme name	Scheme Technology	Status Poush	Total HHs	Total Pop.	Estimated Total Cost (MWF+users)	Expenditure Up to Poush MWF only	GON Estimated	GOF Estimated	Municipality	Users Cash Estimated	Users Kind Estimated	Others Est.
Parbat	Jaljala	6	Thulo Mul DWSS, Jalajala	Gravity	IPO	29	188	2,458,760	885,154	762,216	762,216	245,876	145,000	543,453	-
Parbat	Kushma NP	4	Uttiseni DWS	Gravity	IPC*	28	143	1,305,774	617,706	404,790	404,790	130,577	13,058	352,559	
Parbat	Mahashila	1	Recharge Pond	Dropped	Dropped	0	0	-	-	-	-	-	-	-	-
Parbat	Mahashila	1	Purna Gaun DWSS,Mahashila	Gravity	PPO	36	180	3,600,000	-	1,116,000	1,116,000	360,000	180,000	828,000	
Parbat	Mahashila	1	Horsyandi Lift DWS Scheme	Electrical Lift	IPO	84	665	17,709,594	10,139,926	5,797,787	5,797,787	1,770,959	440,000	3,903,061	-
Parbat	Mahashila	6	Sisnerigadhi Lift DWS, Mahashila	Electrical Lift	IPO	106	620	14,355,498	3,000,000	4,918,695	4,918,695	1,435,548	560,000	2,522,549	
Parbat	Mahashila	4	Tiure Sarthan DWS	Gravity	IPO	72	398	6,880,253	2,270,484	2,132,878	2,132,878	688,025	295,000	1,631,471	
Parbat	Painyu	2	Bhainse Gaira II DWSS, Paiyun 2, Tribeni	Dropped	Dropped	0	0	-	-	-	-	-	-	-	-
Parbat	Painyu	1	Recharge Pond	Dropped	Dropped	0	0	-	-	-	-	-	-	-	-
Parbat	Painyu	7	Dangsing Lift DWSS, Painyu	Electrical Lift	IPO	33	206	6,145,331	-	2,213,430	2,213,430	614,533	165,000	938,937	
Parbat	Painyu	2	Gurase Gaira DWSS, Paiyun	Gravity	IPO	18	111	2,991,850	-	551,361	551,361	188,366	405,000	1,295,762	-
Parbat	Painyu	1	Sisne Gaira DWSS, Paiyun	Gravity	IPO	80	470	5,699,387	-	1,714,343	1,714,343	569,939	405,000	1,295,762	-
Parbat	Painyu	2	Devisthan RWH Scheme	RWH	IPC*	14	117	1,291,823	494,362	468,526	468,526	129,182	12,918	212,671	-
Parbat	Painyu	2	Ghumsing Lift DWS	Electrical Lift	IPO	40	334	7,209,799	3,938,448	2,317,319	2,317,319	720,980	150,000	1,704,181	
Parbat	Phalebas NP	5	Gramin Khanipani	Gravity	IPC*	252	2492	3,954,936	1,890,000	1,046,635	1,332,080	314,827	-	1,261,394	-
Rolpa	Duikholi	6	Dahaghari DWS	Gravity	IPO	24	181	2,499,796	1,153,908	673,907	673,907	249,980	24,998	877,005	-
Rolpa	Lungri	5	Badachaur Dalit basti WSS	Gravity	PPO	31	167	3,225,810	-	1,332,600	667,400	322,580	32,260	870,970	-
Rolpa	Lungri	4	Balale DWSS , Lungri -4	Electrical Lift	PPO	59	386	8,941,317	-	2,781,820	2,781,820	1,500,000	89,413	1,788,263	-
Rolpa	Lungri	3	Simgitha DWSS ,Sirpa , Deurali	Gravity	PPO	120	629	10,466,290	-	2,627,944	2,627,944	1,779,269	104,663	3,326,469	-
Rolpa	Madi	3	Jhimpubang DWS	Solar Lift	IPO	84	461	11,027,054	6,788,135	3,804,334	3,804,334	1,102,705	110,271	2,205,411	-
Rolpa	Madi	4	Jalangkhola Rijabang DWS, Talabang , Madi GP -4	Solar Lift	IPO	75	416	11,411,110	-	3,889,586	3,889,586	1,200,000	114,111	2,317,826	-
Rolpa	Runtigadhi	9	Chandan Simeni WSS	Gravity	IPO	137	738	12,657,866	7,013,496	3,838,529	3,838,529	1,265,787	126,578	3,588,443	-
Rolpa	Runtigadhi	2	Pelpani Gorineta DWS, Runtigadhi-2	Solar Lift	PPC	55	290	8,533,406	-	2,748,213	2,748,213	1,400,000	85,334	1,551,646	-
Rolpa	Runtigadhi	4	Katichap DWS, Runtigadhi-4	Electrical Lift	PPO	92	536	14,330,008	-	4,490,240	4,490,240	2,292,801	143,300	2,913,427	-
Rolpa	Sukidaha	2	Rimulkhola	Solar Lift	IPO	107	663	11,306,678	8,139,386	3,900,804	3,900,804	1,130,668	113,067	2,261,336	-
Rolpa	Sunchhahari	5	Majherikhola	Gravity	IPO	87	540	4,620,166	2,299,104	1,402,771	1,402,771	462,017	46,201	1,306,407	-
Rolpa	Suwarnawoti	3	Taple DWSS , Suwarnawati 3	Solar Lift	PL	56	232	4,446,460	-	1,630,320	769,680	240,000	64,520	1,741,940	-

District	Municipality	Wards	Scheme name	Scheme Technology	Status Poush	Total HHs	Total Pop.	Estimated Total Cost (MWF+users)	Expenditure Up to Poush MWF only	GON Estimated	GOF Estimated	Municipality	Users Cash Estimated	Users Kind Estimated	Others Est.
Rolpa	Suwarnawoti	7	Goldhunga DWSS (Aresh 1 2 3, Suwarnawati 7	Gravity	PPO	169	974	9,616,811	-	2,759,795	2,759,795	1,346,354	96,168	2,654,699	-
Rolpa	Tribeni	2	Mulkhola DWS	Solar Lift	IPC*	32	180	4,904,342	2,817,869	1,659,627	1,659,627	490,434	49,043	1,045,611	-
Rupandehi	Marchawari	1	Semara Deep Tubewell (HandPump) Scheme-2nd	Tube Well	PPC	209	1596	1,635,876	-	588,916	588,916	163,588	16,359	278,099	-
Rupandehi	Sammarimai	4	Farena Deep Tubewell Scheme-2nd	Tube Well	PL	125	625	2,083,000	-	960,000	540,000	208,000	21,000	354,000	-
Rupandehi	Sammarimai	3	Thumahawa Piparhawa OHT	OHT Solar	IPO	302	2593	14,763,556	7,527,326	6,626,617	6,626,617	721,196	14,442	774,683	-
Syangja	Arjunchaupari	5	Panchapuja Bayale Patalbas DWS	Gravity	IPO	75	408	3,678,672	1,257,430	1,140,388	1,140,388	367,867	36,787	993,241	-
Syangja	Arjunchaupari	6	Darau Bhedabari 6-7 DWS	Gravity	IPO	88	511	4,634,594	1,462,846	1,333,923	1,333,923	463,458	1,456,945	46,345	-
Syangja	Arjunchaupari	4	Rapakot DWS	Gravity	PPO	150	985	6,703,338	-	1,809,411	1,809,411	670,334	67,033	2,347,149	-
Syangja	Bhirkot	4	Chhangchhangdi Dalitbasti DWS	Electrical Lift	IPO	72	406	5,356,255	2,286,400	1,655,369	1,655,369	535,626	53,563	1,456,330	-
Syangja	Biruwa	5	Kalisen Bhulbhule Lift DWS	Electrical Lift	IPO	45	366	7,334,869	3,328,850	2,513,706	2,513,706	733,487	73,349	1,500,622	-
Syangja	Biruwa	5	Lausi Niyabari DWSS, Kichanash, 5	Gravity	PPC	22	160	1,379,519	-	367,882	367,882	139,345	504,410	-	-
Syangja	Biruwa	4	Satidanda Bidhyadevi DWS	Gravity	PPO	90	496	5,103,974	-	1,399,492	1,399,492	510,397	51,039	1,743,552	-
Syangja	Biruwa	6	Jhamandanda DWSS, Chinnebas, 6	Gravity	PPO	65	471	4,745,528	-	1,450,860	1,450,860	474,553	47,455	1,321,799	-
Syangja	Chapakot	7	Baradanda DWSS, Sakhar	Solar Lift	PPO	19	109	2,211,789	-	685,654	685,654	221,179	22,118	597,183	-
Syangja	Chapakot	5	Bhandaritol Bhalugaira PSI DWSS	Point Source Improv	IPC	55	314	528,127	262,292	163,719	163,719	52,812	5,281	142,594	-
Syangja	Chapakot	4	Darsing DWS	Gravity	IPO	77	460	7,240,303	1,495,000	2,121,343	2,121,343	724,030	72,403	2,201,185	-
Syangja	Chapakot	6	Gangdimul PSI DWSS, Sakhar 2	Point Source Improv	IPO	11	42	786,963	90,000	120,901	120,901	78,696	7,870	458,596	-
Syangja	Chapakot	7	Kisdi Thulopadhera PSI DWSS, Sakhar 7, 9	Point Source Improv	IPO	55	248	565,636	123,000	175,347	175,347	56,563	5,656	152,722	-
Syangja	Fedikhola	4	Budhiko Pandhero DWS	Electrical Lift	IPO	30	162	2,211,788	796,243	728,107	728,107	221,179	22,118	512,277	-
Syangja	Fedikhola	2	Sarkigaun Salmimuhan DWSS, Fedikhola	Gravity	PPO	30	180	2,280,210	-	706,865	706,865	228,021	22,802	615,657	-
Syangja	Fedikhola	2	Kukhurekhola DWSS, Kukhurekhola, Fedikhola	Gravity	PPO	34	204	2,484,552	-	735,566	735,566	248,455	24,845	740,121	-

District	Municipality	Wards	Scheme name	Scheme Technology	Status Poush	Total HHs	Total Pop.	Estimated Total Cost (MWF+users)	Expenditure Up to Poush MWF only	GON Estimated	GOF Estimated	Municipality	Users Cash Estimated	Users Kind Estimated	Others Est.
Syangja	Fedikhola	1	Chilaunekhola DWSS, Naikhu, Bhoswara, Fedikhola 4	Electrical Lift	PPO	18	108	2,779,445	-	861,628	861,628	277,945	27,794	750,450	-
Syangja	Galyang	8	Mathillo Chiuri DWS	Electrical Lift	IPO	23	128	3,390,927	1,632,780	1,185,402	1,185,402	339,093	33,909	647,122	-
Syangja	Galyang	5	Daunnekhola Baripani DWSS, Nibuwakharka	Gravity	PPC	57	359	2,817,478	-	873,418	873,418	281,748	28,174	760,719	-
Syangja	Galyang	7	Samigaira DWS	Electrical Lift	PPO	154	924	11,024,746	-	3,417,672	3,417,672	1,102,475	110,247	2,976,682	-
Syangja	Harinash	5	Mulyaha Basantedanda DWSS, Chinnebas	Dropped	Dropped	30	135	-	-	-	-	-	-	-	-
Syangja	Harinash	5	Balikot Solar Lift DWSS, Chinnebas	Solar Lift	IPC	51	351	7,460,136	5,055,554	2,414,288	2,414,288	746,014	74,601	1,810,946	-
Syangja	Harinash	4	Dhawakhet Jhiruwash DWSS	Electrical Lift	IPC*	44	287	2,968,552	754,000	1,083,527	1,083,527	296,855	355,336	149,308	-
Syangja	Harinash	1	Kuwapani Bhangjyang DWSS, Kichanas	Electrical Lift	PPO	39	234	4,881,212	-	1,332,066	1,332,066	484,971	31,491	1,700,618	-
Syangja	Harinash	1	Chisapani DWS	Gravity	PPO	196	950	9,591,147	-	2,973,255	2,973,255	959,115	95,911	2,589,610	-
Syangja	Kaligandaki	2	Kutgan Daunne PSIs DWSS, Chandibhnagjyang 1,2	Point Source Improv	IPO	6	36	667,803	200,000	173,624	173,624	66,780	6,678	247,096	-
Syangja	Kaligandaki	3	Bhatikhola DWS	Gravity	IPO	40	302	2,760,002	-	785,883	785,883	276,000	27,600	884,637	-
Syangja	Kaligandaki	6	Bhadarbari Jhirmadi DWS	Electrical Lift	IPO	163	989	10,777,813	4,445,839	3,346,847	3,346,847	1,077,781	107,778	2,898,560	-
Syangja	Kaligandaki	5	Beltari Gofuna DWS	Gravity	PPC	91	559	4,041,778	-	1,144,723	1,144,723	404,178	40,417	1,307,737	-
Syangja	Kaligandaki	5	Bhirkuwa Jhimardi DWSS, Shreekrishnagandaki, 5	Gravity	PPC	121	821	6,897,762	-	1,895,924	1,895,924	689,776	68,977	2,347,160	-
Syangja	Putalibazar	10	Halhale DWSS, Rangbhang, 10	Solar Lift	IPO	23	269	2,492,819	-	884,951	884,951	249,282	24,928	448,707	-
Syangja	Putalibazar	9	Hariyoban Alaichighari DWSS, Kolma, 9	Gravity	IPO	70	439	3,610,514	-	1,041,601	1,041,601	361,051	36,105	1,130,156	-
Syangja	Putalibazar	9	Kolma 5-9 Lift DWS	Electrical Lift	IPO	323	1600	9,905,094	3,499,860	2,436,718	2,436,718	990,509	99,051	3,942,099	-
Syangja	Putalibazar	9	Dahachandyan DWSS, service extension scheme, Kolma, 9	Gravity	PPO	73	438	3,847,257	-	1,105,376	1,105,376	384,725	38,472	1,213,308	-
Syangja	Putalibazar	5	Gudikhola Nuwakot, Putalibazar, 5	Electrical Lift	PPO	198	994	8,567,054	-	2,655,787	2,655,787	856,705	85,671	2,313,105	-
Syangja	Waling	11	Dhanpure PSIs DWSS, Swarek	Point Source Improv	IPO	28	196	409,312	89,000	126,887	126,887	40,931	4,093	110,514	-
Tanahun	Bhanu	6	Devi DWS	Gravity	IPO	52	333	8,254,255	-	2,040,566	2,040,566	825,426	539,809	2,807,887	-
Tanahun	Bhimad	2	Churmurdi Kurlang Kahare DWSS	Gravity	IPO	22	168	3,525,457	709,000	1,003,499	1,003,499	352,546	214,040	951,873	-

District	Municipality	Wards	Scheme name	Scheme Technology	Status Poush	Total HHs	Total Pop.	Estimated Total Cost (MWF+users)	Expenditure Up to Poush MWF only	GON Estimated	GOF Estimated	Municipality	Users Cash Estimated	Users Kind Estimated	Others Est.
Tanahun	Bhimad	5	Aamdanda DWSS	Electrical Lift	IPO	57	343	8,823,970	2,387,766	3,176,629	3,176,629	882,397	587,992	1,000,323	-
Tanahun	Byas	12	Kretasat DWSS	Electrical Lift	IPO	17	101	2,139,692	411,000	579,678	579,678	213,969	179,267	587,099	-
Tanahun	Byas	12	Tamegaira Belghari DWSS	Electrical Lift	IPO	50	241	6,209,260	1,336,000	1,899,682	1,899,682	620,926	512,122	1,276,849	-
Tanahun	Byas	11	Banspani Silkhan DWSS	Electrical Lift	IPO	34	298	7,408,282	3,276,950	2,616,263	2,616,263	740,828	373,898	1,061,031	-
Tanahun	Ghiring	2	Loshadi DWSS	Solar Lift	IPO	12	71	1,951,165	467,000	668,814	668,814	195,117	129,519	288,901	-
Tanahun	Ghiring	2	Andherikhola Sundhara DWSS	Solar Lift	IPO	77	417	6,713,886	1,588,000	2,271,654	2,271,654	671,389	357,829	1,141,361	-
Tanahun	Ghiring	5	Ganadi Kholsi DWSS	Electrical Lift	IPO	53	381	7,591,889	3,887,091	2,480,710	2,480,710	759,189	613,081	1,258,200	-
Tanahun	Ghiring	4	Kot Shavung (Banspani) DWS	Electrical Lift	PPC	83	526	13,033,608	-	4,346,890	4,346,890	1,303,361	987,108	2,049,359	-
Tanahun	Rhishing	6	Patthergaun DWSS	Electrical Lift	IPO	42	382	9,400,060	4,734,071	3,384,022	3,384,022	940,006	94,001	1,598,010	-
Tanahun	Rhishing	2	Todkedi DWSS	Electrical Lift	IPO	165	1228	22,569,010	10,278,148	7,630,608	7,630,608	2,256,901	1,739,575	3,311,318	-
Tanahun	Rhishing	1	Gyaja Wakdip DWS	Electrical Lift	PPC	28	238	3,849,610	-	1,228,456	1,228,456	384,961	339,678	668,059	-
Pyuthan	Airawoti	5	Udik Lift DWS	Electrical Lift	PPO	56	296	4,470,828	-	1,498,538	1,498,538	500,000	44,708	929,044	-
Pyuthan	Airawoti	6	Sanithan Aapkhola DWS	Gravity	PPO	10	47	1,052,314	-	263,907	263,907	105,231	10,523	408,746	-
Pyuthan	Gaumukhi	2	Kathalkhola DWS	Gravity	PPO	191	1281	-	-	-	-	-	-	-	-
Pyuthan	Jhimruk	8	Ratamata DWS	Gravity	IPO	77	424	5,056,679	-	1,372,643	1,372,643	505,668	50,567	1,755,159	-
Pyuthan	Jhimruk	8	Pademela DWS	Gravity	IPO	152	835	7,578,591	2,905,640	1,935,356	1,935,356	757,859	75,786	2,874,234	-
Pyuthan	Mandabi	1	Thakleni DWS	Gravity	IPC*	66	411	5,566,751	2,457,000	1,723,968	1,723,968	556,675	55,668	1,506,472	-
Pyuthan	Naubahini	5	Sakakhola DWS	Gravity	IPO	187	1205	9,314,758	4,032,733	2,668,233	2,668,233	931,476	93,148	2,953,669	-
Pyuthan	Pyuthan	6	Swamifed DWS	Gravity	IPO	51	325	3,292,108	1,050,000	952,944	952,944	331,000	32,921	1,022,299	-
Pyuthan	Pyuthan	6	Bhutbhute DWS	Gravity	IPO	52	310	4,546,345	2,138,055	1,436,297	1,436,297	454,626	45,463	1,173,662	-
Pyuthan	Pyuthan	6	Upallo Satmule DWS	Gravity	IPO	128	730	6,438,768	2,031,000	2,344,624	1,091,000	650,000	64,388	2,288,756	-
Pyuthan	Sarumarani	4	Mainarikhola DWS	Gravity	Dropped	0	0	-	-	-	-	-	-	-	-
Pyuthan	Sarumarani	4	Tallo Tarule DWS	Gravity	IPC*	48	295	8,180,266	3,399,000	2,372,277	2,372,277	818,027	81,803	2,535,883	-
Pyuthan	Sarumarani	4	Dinglang Khola DWS	Electrical Lift	IPO	94	561	9,810,767	-	3,278,832	3,278,832	981,077	98,108	2,173,919	-
Pyuthan	Sworgadwari	3	Odharne DWS	Gravity	IPO	103	571	5,784,554	1,931,190	1,631,189	1,631,189	600,000	57,846	1,864,330	-
Pyuthan	Sworgadwari	3	Bhingri DWS	Electrical Lift	PPO	200	975	6,997,000	-	1,875,000	875,000	417,000	2,750,000	1,080,000	-

RWSSPWN II

Annex 3 Capacity building events and beneficiaries during the reporting period (16.07.2017-14.01.2018)

Annex 3 Capacity building events FY2074/075

SN	District	Municipality	Event Name	Starting Date	Ending Date	Dalit Total	Adibasi Janajati Total	Disadvantaged Terai Caste Total	Religious Minority Total	Other Total	All Total	Total Female	Total Male
1	Arghakhanchi	Malarani	Handwashing Day	15-10-17	15-10-17	21	46	0	0	116	183	106	77
2	Arghakhanchi	Malarani	World Toilet Day	19-11-17	19-11-17	12	12	0	0	74	98	29	69
3	Arghakhanchi	Malarani	WUSC orientation with GESI	27-12-17	27-12-17	10	0	0	0	3	13	6	7
4	Arghakhanchi	Malarani	Procurement of materials	28-12-17	28-12-17	10	0	0	0	3	13	6	7
5	Arghakhanchi	Malarani	Orientation on O&M and WSP++	29-12-17	29-12-17	10	0	0	0	3	13	6	7
6	Arghakhanchi	Malarani	Financial & store management	30-12-17	1/1/2018	10	0	0	0	3	13	6	7
7	Arghakhanchi	Malarani	Step-by-Step training	2/1/2018	2/1/2018	10	0	0	0	3	13	6	7
8	Arghakhanchi	Sitganga	Handwashing Day	15-10-17	15-10-17	23	21	0	0	76	120	77	43
9	Baglung	Bareng	WUSC orientation with GESI	7/12/2017	7/12/2017	0	8	0	0	6	14	7	7
10	Baglung	Bareng	Procurement of materials	8/12/2017	8/12/2017	0	9	0	0	7	16	7	9
11	Baglung	Bareng	Community Action Plan	9/12/2017	10/12/2017	0	9	0	0	6	15	7	8
12	Baglung	Bareng	Orientation on O&M and WSP++	11/12/2017	11/12/2017	0	9	0	0	6	15	7	8
13	Baglung	Bareng	Financial & store management	16-12-17	18-12-17	0	10	0	0	8	18	7	11
14	Baglung	Bareng	Pre-Construction Seminar	13-12-17	13-12-17	1	2	0	0	12	15	7	8
15	Baglung	Bareng	Pre-Construction Seminar	14-12-17	14-12-17	3	1	0	0	9	13	6	7
16	Baglung	Bareng	Handwashing orientation/demonstration	6/12/2017	13-12-17	6	49	0	0	66	121	57	64
17	Baglung	Bareng	World Toilet Day	19-11-17	19-11-17	3	26	0	0	41	70	25	45
18	Baglung	Bareng	During Construction Seminar	7/1/2017	7/1/2017	1	3	0	0	11	15	7	8
19	Baglung	Galkot	Handwashing Day	15-10-17	15-10-17	3	8	0	0	14	25	21	4
20	Baglung	Galkot	WUSC orientation with GESI	25-10-17	25-10-17	5	9	0	0	0	14	5	9
21	Baglung	Galkot	Community Action Plan	26-10-17	27-10-17	6	8	0	0	0	14	4	10
22	Baglung	Galkot	Procurement of materials	28-10-17	28-10-17	4	8	0	0	0	12	4	8
23	Baglung	Galkot	Orientation on O&M and WSP++	29-10-17	29-10-17	4	8	0	0	0	12	4	8
24	Baglung	Galkot	WUSC orientation with GESI	28-11-17	28-11-17	2	8	0	0	1	11	5	6
25	Baglung	Galkot	Orientation on O&M and WSP++	29-11-17	29-11-17	2	8	0	0	1	11	5	6
26	Baglung	Galkot	Procurement of materials	30-11-17	30-11-17	2	9	0	0	1	12	5	7
27	Baglung	Galkot	Financial & store management	1/12/2017	3/12/2017	2	9	0	0	1	12	5	7
28	Baglung	Galkot	Community Action Plan	4/12/2017	5/12/2017	2	9	0	0	1	12	5	7
29	Baglung	Jaimini	WUSC orientation with GESI	20-12-17	20-12-17	11	5	0	0	6	22	9	13
30	Baglung	Jaimini	Procurement of materials	21-12-17	21-12-17	9	4	0	0	4	17	7	10
31	Baglung	Jaimini	Orientation on O&M and WSP++	22-12-17	22-12-17	8	5	0	0	4	17	9	8
32	Baglung	Jaimini	WUSC orientation with GESI	23-12-17	23-12-17	2	3	0	0	10	15	7	8
33	Baglung	Jaimini	Procurement of materials	24-12-17	24-12-17	2	3	0	0	5	10	7	8
34	Baglung	Jaimini	Orientation on O&M and WSP++	25-12-17	25-12-17	2	3	0	0	10	15	7	8
35	Baglung	Jaimini	During Construction Seminar	25-12-17	25-12-17	0	0	0	0	16	16	7	9
36	Baglung	Kathekhola	Handwashing Day	15-10-17	15-10-17	19	9	0	0	11	39	22	17
37	Baglung	Kathekhola	WUSC orientation with GESI	17-10-17	17-10-17	8	0	0	0	6	14	7	7
38	Baglung	Kathekhola	Procurement of materials	31-10-17	31-10-17	9	0	0	0	5	14	6	8
39	Baglung	Kathekhola	Orientation on O&M and WSP++	10/11/2017	10/11/2017	7	0	0	0	5	12	6	6
40	Baglung	Kathekhola	World Toilet Day	19-11-17	19-11-17	13	30	0	0	45	88	54	34
41	Baglung	Kathekhola	Community Action Plan	21-12-17	22-12-17	10	0	0	0	2	12	6	6
42	Baglung	Nishikhola	World Toilet Day			9	51	0	0	2	62	50	12

Annex 3 Capacity building events FY2074/075

SN	District	Municipality	Event Name	Starting Date	Ending Date	Dalit Total	Adibasi Janajati Total	Disadvantaged Terai Caste Total	Religious Minority Total	Other Total	All Total	Total Female	Total Male
43	Baglung	Nishikhola	WUSC orientation with GESI			4	18	0	0	0	22	10	12
44	Baglung	Nishikhola	Financial & store management	1/4/2018	1/6/2018	6	27	0	0	0	33	15	18
45	Baglung	Nishikhola	Financial & store management	1/7/2018	1/7/2018	2	7	0	0	0	9	5	4
46	Baglung	Nishikhola	Financial & store management	1/8/2018	1/8/2018	2	7	0	0	0	9	5	4
47	Baglung	Nishikhola	post contraction training	1/10/2018	1/10/2018	1	10	0	0	0	11	6	5
48	Gulmi	Dhurkot	Handwashing orientation/demonstration	15-10-17	15-10-17	3	17	0	0	30	50	16	34
49	Gulmi	Dhurkot	Post-ODF/Total Sanitation orientation	16-10-17	17-10-17	3	1	0	0	34	38	17	21
50	Gulmi	Dhurkot	Post-ODF/Total Sanitation orientation	29-10-17	30-10-17	1	15	0	0	22	38	13	25
51	Gulmi	Dhurkot	World Toilet Day	19-11-17	19-11-17	27	34	0	0	0	61	28	33
52	Gulmi	Dhurkot	WUSC orientation with GESI	11/12/2017	12/12/2017	3	7	0	0	28	38	18	20
53	Gulmi	Dhurkot	Sanitation & hygiene orientation in school	13-12-17	13-12-17	9	24	0	0	34	67	37	30
54	Gulmi	Dhurkot	Sanitation & hygiene orientation in school	24-12-17	24-12-17	6	46	0	0	8	60	33	27
55	Gulmi	Dhurkot	Sanitation & hygiene orientation in school	24-12-17	24-12-17	8	48	0	0	6	62	34	28
56	Gulmi	Dhurkot	Sanitation & hygiene orientation in school	27-12-17	27-12-17	16	60	0	0	1	77	44	33
57	Gulmi	Dhurkot	Sanitation & hygiene orientation in school	3/1/2018	3/1/2018	6	50	0	0	16	72	39	33
58	Gulmi	Dhurkot	Sanitation & hygiene orientation in school	4/1/2018	4/1/2018	15	29	0	0	26	70	38	32
59	Gulmi	Dhurkot	Sanitation & hygiene orientation in school	5/1/2018	5/1/2018	18	43	0	0	9	70	36	34
60	Gulmi	Ishma	Handwashing Day	15-10-17	15-10-17	20	20	0	0	39	79	52	27
61	Gulmi	Ishma	Post-ODF/Total Sanitation orientation	14-11-17	15-11-17	3	7	0	0	20	30	17	13
62	Gulmi	Ishma	World Toilet Day	19-11-17	19-11-17	11	56	0	0	16	83	42	41
63	Gulmi	Ishma	Post-ODF/Total Sanitation training	2/1/2018	2/1/2018	8	5	0	0	57	70	19	51
64	Gulmi	Kaligandaki	Financial & store management	11/10/2017	13-10-17	6	0	0	0	20	26	10	16
65	Gulmi	Kaligandaki	Post-ODF/Total Sanitation orientation	15-10-17	15-10-17	10	40	0	0	51	101	31	70
66	Gulmi	Kaligandaki	Pre-Construction Seminar	28-10-17	28-10-17	5	0	0	0	29	34	12	22
67	Gulmi	Kaligandaki	Post-ODF/Total Sanitation training	11/11/2017	12/11/2017	5	14	0	0	11	30	21	9
68	Gulmi	Kaligandaki	Other, define	19-11-17	19-11-17	22	59	0	0	22	103	42	61
69	Gulmi	Kaligandaki	WUSC orientation with GESI	24-12-17	25-12-17	0	3	0	0	23	26	15	11
70	Gulmi	Kaligandaki	Post-ODF/Total Sanitation orientation	31-12-17	31-12-17	12	23	0	0	38	73	21	52
71	Gulmi	Kaligandaki	Sanitation & hygiene orientation in school	9/1/2018	9/1/2018	6	18	0	0	48	72	32	40
72	Gulmi	Kaligandaki	Sanitation & hygiene orientation in school	12/1/2018	12/1/2018	21	34	0	0	39	94	47	47
73	Gulmi	Kaligandaki	Sanitation & hygiene orientation in school	14-01-18	14-01-18	12	41	0	0	17	70	43	27
74	Gulmi	Mushikot	Handwashing Day	15-10-17	15-10-17	32	4	0	0	49	85	27	58
75	Gulmi	Mushikot	Pre-Construction Seminar	15-10-17	15-10-17	6	1	0	0	18	25	10	15
76	Gulmi	Mushikot	Community Action Plan	4/11/2017	5/11/2017	10	8	0	0	18	36	6	30
77	Gulmi	Mushikot	World Toilet Day	19-11-17	19-11-17	17	2	0	0	36	55	24	31
78	Gulmi	Mushikot	Womens' Day	4/12/2017	4/12/2017	25	10	0	0	37	75	73	2
79	Gulmi	Mushikot	Post-ODF/Total Sanitation orientation	13-12-17	13-12-17	11	14	0	0	44	69	29	40
80	Gulmi	Mushikot	WUSC orientation with GESI	24-12-17	24-12-17	12	0	0	0	22	34	9	25
81	Gulmi	Mushikot	Pre-Construction Seminar	9/1/2018	9/1/2018	7	9	0	0	12	28	6	22
82	Gulmi	Mushikot	Sanitation & hygiene orientation in school	7/1/2018	8/1/2018	56	58	0	0	55	169	69	100
83	Kapilvastu	Bijayanagar	Handwashing Day	15-10-17	15-10-17	20	17	18	15	19	89	37	52
84	Kapilvastu	Bijayanagar	WUSC orientation with GESI	20-12-17	20-12-17	1	5	3	0	9	18	5	13

Annex 3 Capacity building events FY2074/075

SN	District	Municipality	Event Name	Starting Date	Ending Date	Dalit Total	Adibasi Janajati Total	Disadvantaged Terai Caste Total	Religious Minority Total	Other Total	All Total	Total Female	Total Male
85	Kapilvastu	Bijayanagar	Procurement of materials	2/1/2018	2-Jan	2	14	1	0	19	36	7	29
86	Kapilvastu	Bijayanagar	Other, define	7/1/2018	10/1/2018	2	5	5	3	17	32	0	32
87	Kapilvastu	Kapilvastu	Handwashing Day	15-10-17	15-10-17	22	0	0	0	29	51	32	19
88	Kapilvastu	Kapilvastu	Handwashing Day	15-10-17	15-10-17	10	0	40	3	26	79	46	33
89	Kapilvastu	Kapilvastu	Handwashing Day	15-10-17	15-10-17	7	0	25	2	19	53	23	30
90	Kapilvastu	Kapilvastu	World Toilet Day	19-11-17	19-11-17	11	4	18	27	20	80	52	28
91	Kapilvastu	Kapilvastu	World Toilet Day	19-11-17	19-11-17	9	1	31	16	20	77	63	14
92	Kapilvastu	Kapilvastu	ODF orientation	21-12-17	21-12-17	5	0	18	3	1	27	9	18
93	Kapilvastu	Kapilvastu	ODF orientation	24-12-17	24-12-17	1	0	13	5	7	26	7	19
94	Kapilvastu	Kapilvastu	ODF orientation	30-12-17	30-12-17	3	0	16	2	10	31	3	28
95	Kapilvastu	Kapilvastu	ODF orientation	1/1/2018	1/1/2018	3	0	16	0	13	32	12	20
96	Kapilvastu	Kapilvastu	ODF orientation	1/8/2018	1/8/2018	1	0	12	1	18	32	9	23
97	Kapilvastu	Kapilvastu	WUSC orientation with GESI	1/4/2018	1/4/2018	2	4	0	1	13	20	6	14
98	Kapilvastu	Maharajgunj	Handwashing Day	15-10-17	15-10-17	27	1	44	35	16	123	60	63
99	Kapilvastu	Maharajgunj	World Toilet Day	19-11-17	19-11-17	21	0	102	13	5	141	72	69
100	Kapilvastu	Maharajgunj	Post-ODF/Total Sanitation training	14-12-17	14-12-17	10	0	27	0	3	40	18	22
101	Kapilvastu	Maharajgunj	Post-ODF/Total Sanitation training	14-12-17	14-12-17	10	0	22	6	4	42	25	17
102	Kapilvastu	Maharajgunj	WUSC orientation with GESI	24-11-17	21-12-17	4	0	9	11	2	26	8	18
103	Kapilvastu	Maharajgunj	ODF orientation	23-12-17	24-12-17	9	0	17	6	0	32	19	13
104	Kapilvastu	Maharajgunj	ODF orientation	2/1/2018	3/1/2018	3	0	21	4	4	32	9	23
105	Kapilvastu	Maharajgunj	ODF orientation	28-12-17	29-12-17	5	0	22	4	1	32	10	22
106	Kapilvastu	Maharajgunj	ODF orientation	26-12-17	27-12-17	5	1	23	0	2	31	9	22
107	Kapilvastu	Maharajgunj	ODF orientation	4/1/2018	5/1/2018	7	0	11	4	7	29	7	22
108	Kapilvastu	Maharajgunj	ODF orientation	18-12-17	18-12-17	3	0	34	5	1	43	20	23
109	Kapilvastu	Maharajgunj	ODF orientation	21-12-17	21-12-17	5	0	29	7	0	41	24	17
110	Kapilvastu	Maharajgunj	ODF orientation	18-12-17	18-12-17	0	0	29	3	9	41	22	19
111	Kapilvastu	Mayadevi	Handwashing orientation/demonstration	15-10-17	15-10-17	26	13	20	3	32	94	49	45
112	Kapilvastu	Mayadevi	Other, define	19-11-17	19-11-17	24	6	21	5	26	82	40	42
113	Kapilvastu	Mayadevi	Post-ODF/Total Sanitation orientation	14-11-17	14-11-17	3	10	9	4	12	38	18	20
114	Kapilvastu	Mayadevi	Triggerers' training on sanitation & hygiene	8/1/2018	11/1/2018	5	0	16	5	4	30	6	24
115	Kapilvastu	Mayadevi	Post-ODF/Total Sanitation orientation	19-12-17	19-12-17	3	0	17	2	3	25	11	14
116	Kapilvastu	Mayadevi	Post-ODF/Total Sanitation orientation	24-12-17	24-12-17	5	0	6	8	6	25	6	19
117	Kapilvastu	Mayadevi	Post-ODF/Total Sanitation orientation	28-12-17	28-12-17	7	0	15	10	4	36	7	29
118	Kapilvastu	Suddodhan	Handwashing Day	17-10-17	17-10-17	19	14	80	15	46	174	84	90
119	Kapilvastu	Suddodhan	World Toilet Day	19-11-17	19-11-17	20	17	68	20	39	164	58	106
120	Kapilvastu	Suddodhan		11/12/2017	12/12/2017	5	2	5	2	1	15	6	9
121	Kapilvastu	Suddodhan		14-12-17	15-12-17	5	1	5	3	1	15	4	11
122	Kapilvastu	Suddodhan		17-12-17	18-12-17	4	2	5	2	2	15	8	7
123	Kapilvastu	Suddodhan	WUSC orientation with GESI	28-11-17	28-11-17	3	1	5	0	8	17	7	10
124	Kapilvastu	Suddodhan	WUSC orientation with GESI	2/12/2017	2/12/2017	5	2	7	2	4	20	6	14

Annex 3 Capacity building events FY2074/075

SN	District	Municipality	Event Name	Starting Date	Ending Date	Dalit Total	Adibasi Janajati Total	Disadvantaged Terai Caste Total	Religious Minority Total	Other Total	All Total	Total Female	Total Male
125	Kapilvastu	Suddodhan	WUSC orientation with GESI	16-12-17	16-12-17	2	0	3	10	0	15	4	11
126	Myagdi	Malika	WUSC orientation with GESI	10/10/2017	10/10/2017	3	10	0	0	0	13	5	8
127	Myagdi	Malika	Financial & store management	11/10/2017	13-10-17	3	10	0	0	0	13	6	7
128	Myagdi	Malika	Orientation on O&M and WSP++	14-10-17	14-10-17	3	10	0	0	0	13	6	7
129	Myagdi	Malika	Water Tarriff and Cost Recovery	15-10-17	15-10-17	3	10	0	0	0	13	6	7
130	Myagdi	Malika	Community Action Plan	16-10-17	17-10-17	3	10	0	0	0	13	5	8
131	Myagdi	Malika	WUSC orientation with GESI	10/10/2017	10/10/2017	4	9	0	0	0	13	6	7
132	Myagdi	Malika	Financial & store management	11/10/2017	13-10-17	4	9	0	0	0	13	6	7
133	Myagdi	Malika	Orientation on O&M and WSP++	14-10-17	14-10-17	4	9	0	0	0	13	6	7
134	Myagdi	Malika	Water Tarriff and Cost Recovery	15-10-17	15-10-17	4	9	0	0	0	13	6	7
135	Myagdi	Malika	Community Action Plan	16-10-17	17-10-17	4	9	0	0	0	13	6	7
136	Myagdi	Malika	Handwashing Day	15-10-17	15-10-17	8	34	0	0	1	43	25	18
137	Myagdi	Malika	Handwashing Day	15-10-17	15-10-17	11	31	0	0	0	42	25	17
138	Myagdi	Malika	Handwashing Day	15-10-17	15-10-17	16	8	0	0	17	41	19	22
139	Myagdi	Malika	Handwashing Day	15-10-17	15-10-17	14	30	0	0	0	44	17	27
140	Myagdi	Malika	WUSC orientation with GESI	1/11/2017	1/11/2017	2	8	0	0	0	10	7	3
141	Myagdi	Malika	Financial & store management	2/11/2017	4/11/2017	2	9	0	0	0	11	8	3
142	Myagdi	Malika	Orientation on O&M and WSP++	5/11/2017	5/11/2017	3	9	0	0	0	12	9	3
143	Myagdi	Malika	Water Tarriff and Cost Recovery	6/11/2017	6/11/2017	3	9	0	0	0	12	9	3
144	Myagdi	Malika	Community Action Plan	7/11/2017	8/11/2017	3	9	0	0	0	12	9	3
145	Myagdi	Malika	WUSC orientation with GESI	31-10-17	31-10-17	9	4	0	0	0	13	6	7
146	Myagdi	Malika	Financial & store management	1/11/2017	3/11/2017	9	4	0	0	0	13	6	7
147	Myagdi	Malika	Orientation on O&M and WSP++	4/11/2017	4/11/2017	9	4	0	0	0	13	6	7
148	Myagdi	Malika	Water Tarriff and Cost Recovery	5/11/2017	5/11/2017	9	4	0	0	0	13	6	7
149	Myagdi	Malika	Community Action Plan	6/11/2017	7/11/2017	9	4	0	0	0	13	6	7
150	Myagdi	Malika	Pre-Construction Seminar	30-10-17	30-10-17	5	5	0	0	0	10	7	3
151	Myagdi	Malika	World Toilet Day	19-11-17	19-11-17	10	13	0	0	19	42	20	22
152	Myagdi	Malika	World Toilet Day	19-11-17	19-11-17	15	23	0	0	0	38	19	19
153	Myagdi	Malika	World Toilet Day	19-11-17	19-11-17	9	30	0	0	1	40	28	12
154	Myagdi	Malika	Other, define	3/12/2017	3/12/2017	6	34	0	0	0	40	28	12
155	Myagdi	Malika	Other, define	3/12/2017	3/12/2017	15	17	0	0	0	32	10	22
156	Myagdi	Malika	Other, define	3/12/2017	3/12/2017	27	14	0	0	0	41	24	17
157	Myagdi	Malika	Other, define	10/12/2017	10/12/2017	7	25	0	0	0	32	21	11
158	Myagdi	Malika	Other, define	10/12/2017	10/12/2017	1	40	0	0	1	42	30	12
159	Myagdi	Malika	Other, define	10/12/2017	10/12/2017	8	16	1	0	15	40	19	21
160	Myagdi	Malika	Post-ODF/Total Sanitation orientation	6/12/2017	6/12/2017	4	46	0	0	1	51	25	26
161	Myagdi	Malika	Post-ODF/Total Sanitation orientation	7/12/2017	7/12/2017	12	54	0	0	6	72	35	37
162	Myagdi	Malika	Post-ODF/Total Sanitation orientation	12/12/2017	12/12/2017	28	36	0	0	1	65	38	27
163	Myagdi	Malika	Post-ODF/Total Sanitation orientation	13-12-17	13-12-17	9	58	0	0	2	69	42	27
164	Myagdi	Malika	Post-ODF/Total Sanitation orientation	4/12/2017	4/12/2017	7	37	0	0	0	44	21	23
165	Myagdi	Malika	Post-ODF/Total Sanitation orientation	6/12/2017	6/12/2017	16	34	0	0	0	50	21	29
166	Myagdi	Malika	Post-ODF/Total Sanitation orientation	7/12/2017	7/12/2017	12	20	0	0	0	32	18	14

SN	District	Municipality	Event Name	Starting Date	Ending Date	Dalit Total	Adibasi Janajati Total	Disadvantaged Terai Caste Total	Religious Minority Total	Other Total	All Total	Total Female	Total Male
167	Myagdi	Malika	Post-ODF/Total Sanitation orientation	12/12/2017	12/12/2017	4	54	0	0	0	58	27	31
168	Myagdi	Malika	Post-ODF/Total Sanitation orientation	5/12/2017	5/12/2017	7	25	0	0	9	41	14	27
169	Myagdi	Malika	Post-ODF/Total Sanitation orientation	6/12/2017	6/12/2017	12	27	0	0	8	47	24	23
170	Myagdi	Malika	Post-ODF/Total Sanitation orientation	12/12/2017	12/12/2017	2	43	0	0	2	47	19	28
171	Myagdi	Malika	Post-ODF/Total Sanitation orientation	4/12/2017	4/12/2017	7	35	0	0	1	43	27	16
172	Myagdi	Malika	Post-ODF/Total Sanitation orientation	5/12/2017	5/12/2017	31	11	0	0	5	47	19	28
173	Myagdi	Malika	Post-ODF/Total Sanitation orientation	6/12/2017	6/12/2017	17	29	0	0	10	56	37	19
174	Myagdi	Malika	Post-ODF/Total Sanitation orientation	11/12/2017	11/12/2017	28	38	0	0	1	67	38	29
175	Myagdi	Malika	WUSC orientation with GESI	14-11-17	14-11-17	8	5	0	0	0	13	6	7
176	Myagdi	Malika	Financial & store management	15-11-17	17-11-17	8	5	0	0	0	13	6	7
177	Myagdi	Malika	Orientation on O&M and WSP++	18-11-17	18-11-17	8	5	0	0	0	13	6	7
178	Myagdi	Malika	Water Tarriff and Cost Recovery	19-11-17	19-11-17	8	5	0	0	0	13	6	7
179	Myagdi	Malika	Community Action Plan	21-11-17	21-11-17	8	5	0	0	0	13	6	7
180	Myagdi	Malika	Post-ODF/Total Sanitation training	5/1/2018	5/1/2018	3	15	1	0	11	30	5	25
181	Myagdi	Malika	Post-ODF/Total Sanitation orientation	1/3/2018	1/3/2018	5	2	0	0	8	15	11	4
182	Myagdi	Malika	Post-ODF/Total Sanitation orientation	6/1/2018	6/1/2018	3	11	0	0	1	15	14	1
183	Myagdi	Malika	Post-ODF/Total Sanitation orientation	8/1/2018	8/1/2018	2	7	0	0	6	15	13	2
184	Myagdi	Malika	Post-ODF/Total Sanitation orientation	8/1/2018	8/1/2018	8	7	0	0	0	15	9	6
185	Myagdi	Malika	Post-ODF/Total Sanitation orientation	26-12-17	26-12-17	4	11	0	0	0	15	8	7
186	Myagdi	Malika	Post-ODF/Total Sanitation orientation	27-12-17	27-12-17	0	15	0	0	0	15	12	3
187	Myagdi	Malika	Post-ODF/Total Sanitation orientation	28-12-17	28-12-17	8	8	0	0	0	16	14	2
188	Myagdi	Malika	Post-ODF/Total Sanitation orientation	29-12-17	29-12-17	7	7	0	0	1	15	12	3
189	Myagdi	Malika	Post-ODF/Total Sanitation orientation	30-12-17	30-12-17	8	7	0	0	0	15	13	2
190	Myagdi	Malika	Post-ODF/Total Sanitation orientation	31-12-17	31-12-17	11	4	0	0	0	15	12	3
191	Myagdi	Malika	Post-ODF/Total Sanitation orientation	1/1/2018	1/1/2018	3	12	0	0	0	15	9	6
192	Myagdi	Malika	Post-ODF/Total Sanitation orientation	4/1/2018	4/1/2018	4	11	0	0	0	15	12	3
193	Myagdi	Malika	Post-ODF/Total Sanitation orientation	5/1/2018	5/1/2018	0	15	0	0	0	15	13	2
194	Myagdi	Malika	Post-ODF/Total Sanitation orientation	8/1/2018	8/1/2018	3	11	0	0	1	15	12	3
195	Myagdi	Malika	Post-ODF/Total Sanitation orientation	9/1/2018	9/1/2018	1	11	0	0	3	15	14	1
196	Myagdi	Malika	Post-ODF/Total Sanitation orientation	10/1/2018	10/1/2018	1	4	0	0	10	15	11	4
197	Myagdi	Malika	Post-ODF/Total Sanitation orientation	6/1/2018	6/1/2018	6	9	0	0	0	15	8	7
198	Myagdi	Malika	Post-ODF/Total Sanitation orientation	10/1/2018	10/1/2018	0	15	0	0	0	15	12	3
199	Myagdi	Malika	Post-ODF/Total Sanitation orientation	11/1/2018	11/1/2018	4	11	0	0	0	15	12	3
200	Myagdi	Malika	WUSC orientation with GESI	28-12-17	28-12-17	6	6	0	0	0	12	5	7
201	Myagdi	Malika	Orientation on O&M and WSP++	29-12-17	29-12-17	6	6	0	0	0	12	5	7
202	Myagdi	Malika	Water Tarriff and Cost Recovery	30-12-17	30-12-17	6	6	0	0	0	12	5	7
203	Myagdi	Malika	Financial & store management	31-12-17	2/1/2018	6	6	0	0	0	12	5	7
204	Myagdi	Malika	Community Action Plan	3/1/2018	4/1/2018	6	6	0	0	0	12	5	7
205	Myagdi	Malika	WUSC orientation with GESI	27-12-17	27-12-17	0	9	0	0	1	10	5	5
206	Myagdi	Malika	Financial & store management	28-12-17	30-12-17	0	11	0	0	1	12	7	5
207	Myagdi	Malika	Orientation on O&M and WSP++	31-12-17	31-12-17	0	11	0	0	1	12	7	5
208	Myagdi	Malika	Water Tarriff and Cost Recovery	1/1/2018	1/1/2018	0	11	0	0	1	12	7	5

Annex 3 Capacity building events FY2074/075

SN	District	Municipality	Event Name	Starting Date	Ending Date	Dalit Total	Adibasi Janajati Total	Disadvantaged Terai Caste Total	Religious Minority Total	Other Total	All Total	Total Female	Total Male
209	Myagdi	Malika	Community Action Plan	2/1/2018	4/1/2018	0	11	0	0	1	12	7	5
210	Myagdi	Malika	Post-ODF/Total Sanitation orientation	12/1/2018	12/1/2018	0	14	1	0	0	15	11	4
211	Myagdi	Mangala	Financial & store management	10/10/2017	12/10/2017	4	6	0	0	5	15	5	10
212	Myagdi	Mangala	Financial & store management	10/10/2017	12/10/2017	1	12	0	0	2	15	6	9
213	Myagdi	Mangala	Community Action Plan	15-10-17	16-10-17	4	4	0	0	4	12	5	7
214	Myagdi	Mangala	Community Action Plan	13-10-17	14-10-17	1	9	0	0	2	12	5	7
215	Myagdi	Mangala	WUSC orientation with GESI	13-10-17	13-10-17	4	4	0	0	4	12	5	7
216	Myagdi	Mangala	WUSC orientation with GESI	15-10-17	15-10-17	1	9	0	0	2	12	5	7
217	Myagdi	Mangala	Orientation on O&M and WSP++	14-10-17	14-10-17	4	4	0	0	4	12	5	7
218	Myagdi	Mangala	Orientation on O&M and WSP++	17-10-17	17-10-17	1	9	0	0	2	12	5	7
219	Myagdi	Mangala	Orientation on O&M and WSP++	17-10-17	17-10-17	4	4	0	0	4		5	7
220	Myagdi	Mangala	Orientation on O&M and WSP++	16-10-17	16-10-17	1	9	0	0	2	12	5	7
221	Myagdi	Mangala	Handwashing Day	15-10-17	15-10-17	15	37	0	0	3	55	24	31
222	Myagdi	Mangala	Handwashing Day	15-10-17	15-10-17	37	39	0	0	31	107	45	62
223	Myagdi	Mangala	Handwashing Day	15-10-17	15-10-17	37	12	0	0	13	62	32	30
224	Myagdi	Mangala	Handwashing Day	15-10-17	15-10-17	9	41	0	0	6	56	28	28
225	Myagdi	Mangala	Sanitation & hygiene orientation in school	2/11/2017	2/11/2017	21	15	0	0	9	45	20	25
226	Myagdi	Mangala	Sanitation & hygiene orientation in school	2/11/2017	2/11/2017	18	40	0	0	29	87	39	48
227	Myagdi	Mangala	Sanitation & hygiene orientation in school	3/11/2017	3/11/2017	8	40	0	0	20	68	28	40
228	Myagdi	Mangala	Sanitation & hygiene orientation in school	3/11/2017	3/11/2017	34	62	0	0	25	121	68	53
229	Myagdi	Mangala	Sanitation & hygiene orientation in school	6/11/2017	6/11/2017	25	79	0	0	37	141	75	66
230	Myagdi	Mangala	Sanitation & hygiene orientation in school	8/11/2017	8/11/2017	23	9	0	0	30	62	32	30
231	Myagdi	Mangala	Sanitation & hygiene orientation in school	4/11/2017	4/11/2017	7	39	0	0	1	47	25	22
232	Myagdi	Mangala	Sanitation & hygiene orientation in school	9/11/2017	9/11/2017	26	15	0	0	1	42	22	20
233	Myagdi	Mangala	Sanitation & hygiene orientation in school	10/11/2017	10/11/2017	11	43	0	0	4	58	27	31
234	Myagdi	Mangala	Sanitation & hygiene orientation in school	10/11/2017	10/11/2017	25	34	0	0	19	78	47	31
235	Myagdi	Mangala	Sanitation & hygiene orientation in school	12/11/2017	12/11/2017	8	24	0	0	3	35	21	14
236	Myagdi	Mangala	Sanitation & hygiene orientation in school	9/11/2017	9/11/2017	5	45	0	0	0	50	18	32
237	Myagdi	Mangala	Sanitation & hygiene orientation in school	10/11/2017	10/11/2017	14	28	0	0	0	42	19	23
238	Myagdi	Mangala	Sanitation & hygiene orientation in school	8/11/2017	8/11/2017	4	13	0	0	16	33	19	14
239	Myagdi	Mangala	Sanitation & hygiene orientation in school	12/11/2017	12/11/2017	22	48	0	0	5	75	39	36
240	Myagdi	Mangala	World Toilet Day	19-11-17	19-11-17	12	24	0	0	10	46	20	26
241	Myagdi	Mangala	World Toilet Day	19-11-17	19-11-17	7	8	0	0	19	34	14	20
242	Myagdi	Mangala	World Toilet Day	19-11-17	19-11-17	25	15	0	0	11	51	28	23
243	Myagdi	Mangala	Other, define	3/12/2017	3/12/2017	15	50	0	0	0	65	37	28
244	Myagdi	Mangala	Other, define	3/12/2017	3/12/2017	13	33	0	0	3	49	31	18
245	Myagdi	Mangala	Other, define	3/12/2017	3/12/2017	10	10	0	0	35	55	24	31
246	Myagdi	Mangala	Other, define	10/12/2017	10/12/2017	15	14	0	0	11	40	28	12
247	Myagdi	Mangala	Other, define	10/12/2017	10/12/2017	37	7	0	0	4	48	25	23
248	Myagdi	Mangala	Pre-Construction Seminar	1/12/2017	1/12/2017	2	12	0	0	1	15	7	8
249	Myagdi	Mangala	Pre-Construction Seminar	2/12/2017	2/12/2017	4	11	0	0	0	15	6	9
250	Myagdi	Mangala	Scheme Completion Seminar	1/1/2018	1/1/2018	4	8	0	0	3	15	8	7

Annex 3 Capacity building events FY2074/075

SN	District	Municipality	Event Name	Starting Date	Ending Date	Dalit Total	Adibasi Janajati Total	Disadvantaged Terai Caste Total	Religious Minority Total	Other Total	All Total	Total Female	Total Male
251	Myagdi	Mangala	Scheme Completion Seminar	1/1/2018	1/1/2018	5	4	0	0	6	15	5	10
252	Myagdi	Mangala	Scheme Completion Seminar	3/1/2018	3/1/2018	5	2	0	0	8	15	5	10
253	Myagdi	Mangala	Scheme Completion Seminar	5/1/2018	5/1/2018	7	6	0	0	2	15	8	7
254	Myagdi	Mangala	Scheme Completion Seminar	7/1/2018	7/1/2018	2	12	0	0	1	15	9	6
255	Myagdi	Mangala	Scheme Completion Seminar	7/1/2018	7/1/2018	3	4	0	0	8	15	6	9
256	Myagdi	Mangala	Other, define	2/1/2018	2/1/2018	4	8	0	0	3	15	8	7
257	Myagdi	Mangala	Other, define	2/1/2018	2/1/2018	2	4	0	0	9	15	5	10
258	Myagdi	Mangala	Other, define	4/1/2018	4/1/2018	7	1	0	0	7	15	5	10
259	Myagdi	Mangala	Other, define	6/1/2018	6/1/2018	7	6	0	0	2	15	6	9
260	Myagdi	Mangala	Other, define	8/1/2018	8/1/2018	4	10	0	0	1	15	7	8
261	Myagdi	Mangala	Other, define	8/1/2018	8/1/2018	3	4	0	0	8	15	6	9
262	Myagdi	Mangala	Orientation on social marketing	4/1/2018	4/1/2018	3	6	1	0	15	25	6	19
263	Myagdi	Mangala	Mason training on biogas and improved cooking stoves	6/1/2018	11/1/2018	9	9	0	0	2	20	11	9
264	Nawalparasi	Bulingtar	Sanitation & hygiene orientation in school	15-10-17	15-10-17	33	198	0	0	134	365	186	179
265	Nawalparasi	Bulingtar	WUSC orientation with GESI	28-11-17	28-11-17	9	11	0	0	5	25	14	11
266	Nawalparasi	Bulingtar	WUSC orientation with GESI	30-11-17	30-11-17	6	14	0	0	2	22	12	10
267	Nawalparasi	Bulingtar	Financial & store management	20-12-17	21-12-17	3	11	0	0	3	17	8	9
268	Nawalparasi	Bulingtar	Procurement of materials	22-12-17	22-12-17	3	11	0	0	3	17	8	9
269	Nawalparasi	Bulingtar	Orientation on O&M and WSP++	24-12-17	24-12-17	8	10	0	0	2	20	13	7
270	Nawalparasi	Bulingtar	Orientation on O&M and WSP++	25-12-17	25-12-17	7	13	0	0	1	21	11	10
271	Nawalparasi	Bulingtar	Community Action Plan	29-12-17	30-12-17	6	14	0	0	1	21	9	12
272	Nawalparasi	Bulingtar	Community Action Plan	2/1/2018	3/1/2018	4	11	0	0	5	20	7	13
273	Nawalparasi	Bulingtar	During Construction Seminar	31-12-17	31-12-17	9	12	0	0	0	21	10	11
274	Nawalparasi	Bulingtar	Financial & store management	20-12-17	21-12-17	8	11	0	0	2	21	12	9
275	Nawalparasi	Bulingtar	Procurement of materials	22-12-17	22-12-17	8	11	0	0	2	21	12	9
276	Nawalparasi	Gaindakot	Handwashing Day	15-10-17	15-10-17	8	104	0	0	20	132	73	59
277	Nawalparasi	Gaindakot	WUSC orientation with GESI	11/6/2017	11/6/2017	0	18	0	0	0	18	9	9
278	Nawalparasi	Gaindakot	Financial & store management	11/7/2017	11/8/2017	0	18	0	0	0	18	9	9
279	Nawalparasi	Gaindakot	Orientation on O&M and WSP++	11/10/2017	11/10/2017	0	17	0	0	0	17	8	9
280	Nawalparasi	Gaindakot	Community Action Plan	11/11/2017	11/12/2017	0	19	0	0	0	19	9	10
281	Nawalparasi	Gaindakot	Procurement Materials	11/9/2017	11/9/2017	0	18	0	0	0	18	9	9
282	Nawalparasi	Gaindakot	World Toilet Day	19-09-17	19-09-17	3	72	0	0	24	99	60	39
283	Nawalparasi	Gaindakot	WUSC orientation with GESI	22-09-17	22-09-17	0	16	0	0	0	16	7	9
284	Nawalparasi	Gaindakot	Financial & store management	23-09-17	24-09-17	0	16	0	0	0	16	7	9
285	Nawalparasi	Gaindakot	Procurement of materials	25-09-17	25-09-17	0	16	0	0	0	16	7	9
286	Nawalparasi	Gaindakot	Orientation on O&M and WSP++	26-09-17	26-09-17	0	15	0	0	0	15	6	9
287	Nawalparasi	Gaindakot	Community Action Plan	27-09-17	28-09-17	0	17	0	0	0	17	7	10
288	Nawalparasi	Gaindakot	Post-ODF/Total Sanitation orientation	43107	43107	1	15	0	0	27	43	38	5
289	Nawalparasi	Gaindakot	Post-ODF/Total Sanitation training	43105	43105	3	9	0	0	22	34	9	25
290	Nawalparasi	Madhyabindu	Handwashing Day	15-10-17	15-10-17	2	38	0	0	15	55	46	9
291	Nawalparasi	Madhyabindu	World Toilet Day	15-11-17	15-11-17	8	56	0	0	11	75	38	37

Annex 3 Capacity building events FY2074/075

SN	District	Municipality	Event Name	Starting Date	Ending Date	Dalit Total	Adibasi Janajati Total	Disadvantaged Terai Caste Total	Religious Minority Total	Other Total	All Total	Total Female	Total Male
292	Nawalparasi	Madhyabindu	Training to mother group,child club and others	15-12-17	15-12-17	3	19	0	0	30	52	42	10
293	Nawalparasi	Madhyabindu	WUSC orientation with GESI	21-12-17	21-12-17	0	21	0	0	15	36	12	24
294	Nawalparasi	Madhyabindu	Financial & store management	20-12-17	22-12-17	0	21	0	0	12	33	12	21
295	Nawalparasi	Madhyabindu	Orientation on O&M and WSP++	19-12-17	19-12-17	0	19	0	0	21	40	19	21
296	Nawalparasi	Madhyabindu	Community Action Plan	23-12-17	23-12-17	0	24	0	0	12	36	15	21
297	Nawalparasi	Madhyabindu	Post-ODF/Total Sanitation orientation	1/12/2018	1/12/2018	1	36	0	0	19	56	32	24
298	Nawalparasi	Ramgram	Other, define	20-09-17	20-09-17	3	3	14	3	4	27	5	22
299	Nawalparasi	Ramgram	Other, define	20-09-17	20-09-17	5	13	4	0	12	34	14	20
300	Nawalparasi	Ramgram	Handwashing Day	15-10-17	15-10-17	6	45	42	2	8	103	64	39
301	Nawalparasi	Ramgram	Post-ODF/Total Sanitation orientation	10/11/2017	10/11/2017	3	2	14	1	5	25	6	19
302	Nawalparasi	Ramgram	Post-ODF/Total Sanitation orientation	13-11-17	13-11-17	3	8	4	0	7	22	10	12
303	Nawalparasi	Ramgram	Other, define	28-12-17	28-12-17	3	13	17	4	7	44	10	34
304	Nawalparasi	Ramgram	Other, define	2/1/2018	2/1/2018	7	8	21	0	3	39	33	6
305	Nawalparasi	Ramgram	Other, define	3/1/2018	3/1/2018	6	2	14	2	5	29	13	16
306	Nawalparasi	Ramgram	Post-ODF/Total Sanitation orientation	8/1/2018	8/1/2018	5	18	3	0	1	27	25	2
307	Nawalparasi	Ramgram	Post-ODF/Total Sanitation orientation	10/1/2018	10/1/2018	8	3	11	4	1	27	24	3
308	Nawalparasi	Sarawal	Other, define	8/11/2017	8/11/2017	2	11	11	1	5	30	12	18
309	Nawalparasi	Sarawal	Other, define	17-11-17	17-11-17	2	25	2	0	5	34	21	13
310	Nawalparasi	Sarawal	Other, define	19-11-17	19-11-17	4	19	6	0	3	32	18	14
311	Nawalparasi	Sarawal	Post-ODF/Total Sanitation orientation	12/1/2018	12/1/2018	0	32	0	0	8	40	33	7
312	Nawalparasi	Sarawal	WUSC orientation with GESI	25-12-17	25-12-17	1	14	1	0	1	17	7	10
313	Nawalparasi	Sarawal	Financial & store management	27-12-17	28-12-17	1	14	1	0	1	17	7	10
314	Nawalparasi	Sarawal	Orientation on O&M and WSP++	26-12-17	26-12-17	1	14	1	0	1	17	7	10
315	Nawalparasi	Sarawal	Community Action Plan	29-12-17	29-12-17	1	14	1	0	1	17	7	10
316	Parbat	Bihadi	WUSC orientation with GESI	8/1/2017	8/1/2017	2	9	0	0	2	13	5	8
317	Parbat	Bihadi	Procurement of materials	8/2/2017	8/2/2017	2	9	0	0	2	13	5	8
318	Parbat	Bihadi	Financial & store management	8/3/2017	8/4/2017	2	9	0	0	2	13	5	8
319	Parbat	Bihadi	Orientation on O&M and WSP++	8/5/2017	8/5/2017	2	9	0	0	2	13	5	8
320	Parbat	Bihadi	Community Action Plan	8/6/2017	8/7/2017	2	9	0	0	2	13	5	8
321	Parbat	Bihadi	WUSC orientation with GESI	9/10/2017	9/10/2017	1	0	0	0	10	11	4	7
322	Parbat	Bihadi	Procurement of materials	10/10/2017	10/10/2017	1	0	0	0	10	11	4	7
323	Parbat	Bihadi	Financial & store management	11/10/2017	12/10/2017	1	0	0	0	10	11	4	7
324	Parbat	Bihadi	Orientation on O&M and WSP++	13-10-17	13-10-17	1	0	0	0	10	11	4	7
325	Parbat	Bihadi	Community Action Plan	14-10-17	14-10-17	1	0	0	0	10	11	4	7
326	Parbat	Bihadi	Handwashing Day	15-10-17	15-10-17	0	7	0	0	31	38	14	24
327	Parbat	Bihadi	WUSC orientation with GESI	11/12/2017	11/12/2017	0	0	0	0	11	11	5	6
328	Parbat	Bihadi	Financial & store management	25-12-17	26-12-17	1	0	0	0	12	13	7	6
329	Parbat	Bihadi	Procurement of materials	27-12-17	27-12-17	1	0	0	0	12	13	7	6
330	Parbat	Bihadi	Orientation on O&M and WSP++	28-12-17	28-12-17	1	0	0	0	12	13	7	6
331	Parbat	Bihadi	Community Action Plan	15-12-17	15-12-17	1	1	0	0	11	13	6	7
332	Parbat	Bihadi	Community Mapping	16-12-17	16-12-17	1	1	0	0	11	13	6	7

SN	District	Municipality	Event Name	Starting Date	Ending Date	Dalit Total	Adibasi Janajati Total	Disadvantaged Terai Caste Total	Religious Minority Total	Other Total	All Total	Total Female	Total Male
333	Parbat	Bihadi	Master training of trainers on post-ODF/Total Sanitation	7/1/2018	7/1/2018	4	4	4	0	24	36	8	28
334	Parbat	Jaljala	WUSC orientation with GESI	7/11/2017	7/11/2017	2	10	0	0	1	13	6	7
335	Parbat	Jaljala	Procurement of materials	8/11/2017	8/11/2017	2	10	0	0	1	13	6	7
336	Parbat	Jaljala	Financial & store management	10/11/2017	11/11/2017	2	10	0	0	1	13	6	7
337	Parbat	Jaljala	Orientation on O&M and WSP++	9/11/2017	9/11/2017	2	10	0	0	1	13	6	7
338	Parbat	Jaljala	Community Action Plan	12/11/2017	12/11/2017	2	10	0	0	1	13	6	7
339	Parbat	Mahashila	Signature on agreement letter programme	6/8/2017	6/8/2017	5	4	0	0	28	37	8	29
340	Parbat	Mahashila	Post-ODF/Total Sanitation orientation	30-07-17	30-07-17	22	10	0	0	2	34	16	18
341	Parbat	Mahashila	Post-ODF/Total Sanitation orientation	31-07-17	31-07-17	5	20	0	0	2	27	19	8
342	Parbat	Mahashila	Post-ODF/Total Sanitation orientation	1/8/2017	1/8/2017	4	9	0	0	9	22	11	11
343	Parbat	Mahashila	Post-ODF/Total Sanitation orientation	2/8/2017	2/8/2017	1	13	0	0	10	24	8	16
344	Parbat	Mahashila	Post-ODF/Total Sanitation orientation	3/8/2017	3/8/2017	8	13	0	0	13	34	16	18
345	Parbat	Mahashila	Post-ODF/Total Sanitation orientation	4/8/2017	4/8/2017	1	7	0	0	13	21	10	11
346	Parbat	Mahashila	Post-ODF/Total Sanitation orientation	5/8/2017	5/8/2017	4	20	0	0	25	49	25	24
347	Parbat	Mahashila	Post-ODF/Total Sanitation orientation	6/8/2017	6/8/2017	2	11	0	0	10	23	3	20
348	Parbat	Mahashila	Post-ODF/Total Sanitation orientation	31-08-17	31-08-17	4	20	0	0	16	40	16	24
349	Parbat	Mahashila	Post-ODF/Total Sanitation orientation	1/9/2017	1/9/2017	0	10	0	0	17	27	12	15
350	Parbat	Mahashila	Post-ODF/Total Sanitation orientation	2/9/2017	2/9/2017	1	6	0	0	10	17	4	13
351	Parbat	Mahashila	WUSC orientation with GESI	10/10/2017	10/10/2017	15	0	0	0	0	15	6	9
352	Parbat	Mahashila	Financial & store management	11/10/2017	11/10/2017	15	0	0	0	0	15	6	9
353	Parbat	Mahashila	Procurement of materials	13-10-17	13-10-17	15	0	0	0	0	15	6	9
354	Parbat	Mahashila	Orientation on O&M and WSP++	14-10-17	14-10-17	15	0	0	0	0	15	6	9
355	Parbat	Mahashila	Community Action Plan	15-10-17	15-10-17	15	0	0	0	0	15	6	9
356	Parbat	Mahashila	Handwashing Day	17-10-17	17-10-17	55	20	0	0	56	131	61	70
357	Parbat	Mahashila	During Construction Seminar	21-12-17	21-12-17	2	0	0	0	13	15	6	9
358	Parbat	Mahashila	Pump Operators training	27-12-17	31-12-17	3	3	0	0	6	12	0	12
359	Parbat	Mahashila	Post-ODF/Total Sanitation training	3/1/2018	3/1/2018	5	6	0	0	21	32	5	27
360	Parbat	Mahashila	Pre-Construction Seminar	12/1/2018	12/1/2018	15	0	0	0	0	15	6	9
361	Parbat	Painyu		4/8/2017	4/8/2017	1	5	0	0	25	31	13	18
362	Parbat	Painyu	WUSC orientation with GESI	10/10/2017	10/10/2017	0	0	0	0	8	8	4	4
363	Parbat	Painyu	Procurement of materials	11/10/2017	11/10/2017	0	0	0	0	8	8	4	4
364	Parbat	Painyu	Orientation on O&M and WSP++	12/10/2017	12/10/2017	0	0	0	0	8	8	4	4
365	Parbat	Painyu	Community Action Plan	13-10-17	14-10-17	0	0	0	0	7	7	3	4
366	Parbat	Painyu	Financial & store management	15-10-17	16-10-17	0	0	0	0	7	7	3	4
367	Parbat	Painyu	WUSC orientation with GESI	23-10-17	23-10-17	1	0	0	0	9	10	4	6
368	Parbat	Painyu	Procurement of materials	24-10-17	24-10-17	1	0	0	0	9	10	4	6
369	Parbat	Painyu	Orientation on O&M and WSP++	25-10-17	25-10-17	1	0	0	0	9	10	4	6
370	Parbat	Painyu	Community Action Plan	26-10-17	27-10-17	1	0	0	0	9	10	4	6
371	Parbat	Painyu	Financial & store management	28-10-17	29-10-17	1	0	0	0	9	10	4	6
372	Parbat	Painyu	WUSC orientation with GESI	2/1/2018	2/1/2018	1	3	0	0	3	7	3	4
373	Parbat	Painyu	Procurement of materials	3/1/2018	3/1/2018	1	3	0	0	3	7	3	4

Annex 3 Capacity building events FY2074/075

SN	District	Municipality	Event Name	Starting Date	Ending Date	Dalit Total	Adibasi Janajati Total	Disadvantaged Terai Caste Total	Religious Minority Total	Other Total	All Total	Total Female	Total Male
374	Parbat	Painyu	Orientation on O&M and WSP++	4/1/2018	4/1/2018	1	3	0	0	3	7	3	4
375	Parbat	Painyu	Community Action Plan	5/1/2018	6/1/2018	1	3	0	0	3	7	3	4
376	Parbat	Painyu	Financial & store management	7/1/2018	8/1/2018	1	3	0	0	3	7	3	4
377	Pyuthan	Jhimruk	Handwashing Day	5/10/2017	5/10/2017	4	5	0	0	24	33	10	23
378	Pyuthan	Jhimruk	WUSC orientation with GESI	5/11/2017	5/11/2017	1	0	0	0	27	28	12	16
379	Pyuthan	Jhimruk	Orientation on O&M and WSP++	6/11/2017	6/11/2017	2	0	0	0	23	25	16	9
380	Pyuthan	Jhimruk	Community Action Plan	7/11/2017	8/11/2017	1	0	0	0	23	24	13	11
381	Pyuthan	Jhimruk	Financial & store management	9/11/2017	11/11/2017	1	0	0	0	26	27	13	14
382	Pyuthan	Jhimruk	Pre-Construction Seminar	1/10/2018	1/10/2018	2	0	0	0	19	21	14	7
383	Pyuthan	Pyuthan	WUSC orientation with GESI	15-10-17	15-10-17	0	13	0	0	3	16	7	9
384	Pyuthan	Pyuthan	Handwashing Day	15-10-17	15-10-17	2	16	0	0	17	35	11	24
385	Pyuthan	Pyuthan	Orientation on O&M and WSP++	16-10-17	16-10-17	0	12	0	0	3	15	7	8
386	Pyuthan	Pyuthan	WUSC orientation with GESI	26-10-17	26-10-17	1	13	0	0	3	17	6	11
387	Pyuthan	Pyuthan	Orientation on O&M and WSP++	27-10-17	27-10-17	1	13	0	0	4	18	7	11
388	Pyuthan	Pyuthan	Community Action Plan	30-10-17	31-10-17	0	12	0	0	4	16	6	10
389	Pyuthan	Pyuthan	Community Action Plan	1/11/2017	1/11/2017	1	9	0	0	5	15	6	9
390	Pyuthan	Pyuthan	Financial & store management	3/11/2017	4/11/2017	0	17	0	0	5	22	8	14
391	Pyuthan	Pyuthan	World Toilet Day	19-11-17	19-11-17	3	32	0	0	5	40	23	17
392	Pyuthan	Sarumarani	Handwashing Day	10/5/2017	10/5/2017	20	27	0	7	29	83	41	42
393	Pyuthan	Sarumarani	WUSC orientation with GESI	25-10-17	25-10-17	0	11	0	0	2	13	7	6
394	Pyuthan	Sarumarani	Orientation on O&M and WSP++	26-10-17	26-10-17	0	11	0	0	2	13	7	6
395	Pyuthan	Sarumarani	Financial & store management	27-10-17	29-10-17	0	32	0	0	9	41	14	27
396	Pyuthan	Sarumarani	Community Action Plan	30-10-17	31-10-17	0	30	0	0	4	34	14	20
397	Pyuthan	Sarumarani	Other, define			16	44	0	0	0	60	31	29
398	Pyuthan	Sworgadwari	Handwashing Day	15-10-17	15-10-17	5	1	0	1	23	30	11	19
399	Pyuthan	Sworgadwari	WUSC orientation with GESI	28-10-17	28-10-17	4	13	0	0	1	18	8	10
400	Pyuthan	Sworgadwari	Orientation on O&M and WSP++	29-10-17	29-10-17	5	13	0	0	1	19	8	11
401	Pyuthan	Sworgadwari	Financial & store management	1/11/2017	3/11/2017	3	14	0	0	1	18	9	9
402	Pyuthan	Sworgadwari	Community Action Plan	6/11/2017	7/11/2017	3	12	0	0	2	17	8	9
403	Pyuthan	Sworgadwari	Scheme Completion Seminar	11/8/2017	12/8/2017	3	8	0	0	9	20	9	11
404	Pyuthan	Sworgadwari	Handwashing orientation/demonstration	2/11/2017	2/11/2017	7	38	0	0	3	48	24	24
405	Pyuthan	Sworgadwari	Pre-Construction Seminar	24-11-17	24-11-17	2	15	0	0	1	18	9	9
406	Pyuthan	Sworgadwari	Handwashing orientation/demonstration	20-11-17	20-11-17	7	28	0	0	31	66	36	30
407	Pyuthan	Sworgadwari	WSP++ Training and Preparation	2/1/2018	4/1/2018	2	0	0	0	15	17	10	7
408	Rolpa	Madi	WUSC orientation with GESI	2/12/2017	2/12/2017	0	15	0	0	0	15	7	8
409	Rolpa	Madi	Orientation on O&M and WSP++	3/12/2017	4/12/2017	1	14	0	0	0	15	7	8
410	Rolpa	Madi	Financial & store management	5/12/2017	6/12/2017	1	14	0	0	0	15	7	8
411	Rolpa	Madi	Community Action Plan	7/12/2017	8/12/2017	1	14	0	0	0	15	7	8
412	Rolpa	Madi	Procurement of materials	9/12/2017	9/12/2017	1	14	0	0	0	15	7	8
413	Rolpa	Madi	Orientation on O&M and WSP++	12/12/2017	14-12-17	1	1	0	0	9	11	4	7
414	Rupandehi	Gaidahawa	Handwashing Day	15-10-17	15-10-17	23	9	29	6	5	72	20	52
415	Rupandehi	Lumbini Sanskritik	Handwashing Day	15-10-17	15-10-17	16	0	27	0	12	55	17	38

Annex 3 Capacity building events FY2074/075

SN	District	Municipality	Event Name	Starting Date	Ending Date	Dalit Total	Adibasi Janajati Total	Disadvantaged Terai Caste Total	Religious Minority Total	Other Total	All Total	Total Female	Total Male
416	Rupandehi	Lumbini Sanskritik	Handwashing Day	15-10-17	15-10-17	15	0	36	16	0	67	17	50
417	Rupandehi	Lumbini Sanskritik	Handwashing Day	15-10-17	15-10-17	7	4	33	13	0	57	13	44
418	Rupandehi	Lumbini Sanskritik	Handwashing Day	15-10-17	15-10-17	5	2	28	7	8	50	18	32
419	Rupandehi	Marchawari	Handwashing Day	15-10-17	15-10-17	11	0	36	2	5	54	15	39
420	Rupandehi	Marchawari	Handwashing Day	15-10-17	15-10-17	10	0	40	0	1	51	16	35
421	Rupandehi	Marchawari	World Toilet Day	19-11-17	19-11-17	17	0	123	3	3	146	74	72
422	Rupandehi	Marchawari	WUSC orientation with GESI	1/2/2017	1/2/2017	2	0	12	0	0	14	7	7
423	Rupandehi	Marchawari	Financial & store management	1/3/2017	1/3/2017	2	0	12	0	0	14	7	7
424	Rupandehi	Marchawari	Procurement of materials	1/4/2017	1/4/2017	3	0	12	0	0	15	8	7
425	Rupandehi	Marchawari	Orientation on O&M and WSP++	1/5/2017	1/5/2017	3	0	13	0	0	16	8	8
426	Rupandehi	Sammarimai	Handwashing Day	15-10-17	15-10-17	21	0	22	5	20	68	16	52
427	Rupandehi	Sammarimai	Toilet day	19-11-17	19-11-17	24	21	49	7	12	113	43	70
428	Syangja	Arjunchaupari	Handwashing Day	15-10-17	15-10-17	9	21	0	0	16	46	29	17
429	Syangja	Arjunchaupari	World Toilet Day	19-12-17	19-12-17	13	3	0	0	37	53	10	43
430	Syangja	Biruwa	Handwashing Day	15-10-17	15-10-17	5	42	0	0	5	52	34	18
431	Syangja	Biruwa	World Toilet Day	19-12-17	19-12-17	0	52	0	0	12	64	45	19
432	Syangja	Biruwa	Community Mapping	1/1/2018	1/1/2018	0	1	0	0	11	12	4	8
433	Syangja	Biruwa	WUSC orientation with GESI	1/2/2018	1/2/2018	0	1	0	0	11	12	4	8
434	Syangja	Biruwa	Financial & store management	1/3/2018	1/3/2018	0	1	0	0	11	12	4	8
435	Syangja	Biruwa	Procurement of materials	1/4/2018	1/4/2018	0	1	0	0	11	12	4	8
436	Syangja	Biruwa	Orientation on O&M and WSP++	1/5/2018	1/5/2018	0	1	0	0	11	12	4	8
437	Syangja	Chapkot	Handwashing Day	15-10-17	15-10-17	47	83	0	0	120	250	126	124
438	Syangja	Chapkot	Pre-Construction Seminar	13-09-17	13-09-17	2	1	0	0	12	15	10	5
439	Syangja	Chapkot	Pre-Construction Seminar	24-10-17	24-10-17	0	7	0	0	0	7	4	3
440	Syangja	Chapkot	World Toilet Day	19-11-17	19-11-17	27	88	0	2	89	206	117	89
441	Syangja	Fedikhola	Handwashing Day	15-10-17	15-10-17	25	1	0	0	9	35	23	12
442	Syangja	Fedikhola	WUSC orientation with GESI	5/11/2017	11/5/2017	1	0	0	0	14	15	7	8
443	Syangja	Fedikhola	Financial & store management	6/11/2017	11/6/2017	1	0	0	0	14	15	7	8
444	Syangja	Fedikhola	Procurement of materials	7/11/2017	11/7/2017	1	0	0	0	14	15	7	8
445	Syangja	Fedikhola	Orientation on O&M and WSP++	8/11/2017	11/8/2017	1	0	0	0	14	15	7	8
446	Syangja	Fedikhola	Community Action Plan	9/11/2017	11/9/2017	1	0	0	0	14	15	7	8
447	Syangja	Fedikhola	World Toilet Day	19-12-17	19-12-17	10	0	0	0	47	57	27	30
448	Syangja	Galyang	Handwashing Day	15-10-17	15-10-17	0	28	0	0	59	87	46	41
449	Syangja	Galyang	World Toilet Day	19-11-17	19-11-17	2	8	0	0	27	37	16	21
450	Syangja	Galyang	Other, define	29-11-17	29-11-17	38	12	0	0	56	106	72	34
451	Syangja	Galyang	During Construction Seminar	28-12-17	28-12-17	0	21	0	0	0	21	12	9
452	Syangja	Harinas	WSP++ Training and Preparation	21-11-17	23-11-17	1	12	0	0	0	13	5	8
453	Syangja	Harinas	World Toilet Day	19-11-17	19-11-17	3	18	0	0	11	32	16	16
454	Syangja	Kaligandaki	Handwashing Day	15-10-17	15-10-17	26	40	0	0	13	79	41	38
455	Syangja	Kaligandaki	World Toilet Day	19-11-17	19-11-17	0	50	0	0	1	51	29	22
456	Syangja	Kaligandaki	Financial & store management	15-11-17	15-11-17	0	7	0	0	0	7	4	3
457	Syangja	Kaligandaki	Procurement of materials	16-11-17	16-11-17	0	7	0	0	0	7	4	3

Annex 3 Capacity building events FY2074/075

SN	District	Municipality	Event Name	Starting Date	Ending Date	Dalit Total	Adibasi Janajati Total	Disadvantaged Terai Caste Total	Religious Minority Total	Other Total	All Total	Total Female	Total Male
458	Syangja	Kaligandaki	WUSC orientation with GESI	17-11-17	17-11-17	0	7	0	0	0	7	4	3
459	Syangja	Kaligandaki	Financial & store management	19-11-17	19-11-17	0	16	0	0	1	17	9	8
460	Syangja	Kaligandaki	Procurement of materials	20-11-17	20-11-17	0	16	0	0	1	17	9	8
461	Syangja	Kaligandaki	Orientation on O&M and WSP++	21-11-17	21-11-17	0	16	0	0	1	17	9	8
462	Syangja	Kaligandaki	Community Action Plan	22-11-17	22-11-17	0	16	0	0	1	17	9	8
463	Syangja	Kaligandaki	Community Mapping	23-11-17	23-11-17	0	16	0	0	1	17	9	8
464	Syangja	Kaligandaki	WUSC orientation with GESI	3/1/2018	3/1/2018	0	0	0	0	31	31	17	14
465	Syangja	Kaligandaki	Financial & store management	4/1/2018	4/1/2018	0	0	0	0	31	31	17	14
466	Syangja	Kaligandaki	Procurement of materials	5/1/2018	5/1/2018	0	0	0	0	31	31	17	14
467	Syangja	Kaligandaki	Orientation on O&M and WSP++	6/1/2018	6/1/2018	0	0	0	0	31	31	17	14
468	Syangja	Kaligandaki	Community Action Plan	7/1/2018	7/1/2018	0	0	0	0	31	31	17	14
469	Syangja	Putalibazar	Handwashing Day	15-10-17	15-10-17	12	29	0	0	29	70	50	20
470	Syangja	Putalibazar	World Toilet Day	19-11-17	19-11-17	17	38	0	0	29	84	34	50
471	Syangja	Putalibazar	WUSC orientation with GESI	25-12-17	25-12-17	0	20	0	0	0	20	8	12
472	Syangja	Putalibazar	Financial & store management	26-12-17	26-12-17	0	20	0	0	0	20	8	12
473	Syangja	Putalibazar	Procurement of materials	27-12-17	27-12-17	0	20	0	0	0	20	8	12
474	Syangja	Putalibazar	Orientation on O&M and WSP++	28-12-17	28-12-17	0	20	0	0	0	20	8	12
475	Syangja	Putalibazar	Community Action Plan	29-12-17	29-12-17	0	20	0	0	0	20	8	12
476	Syangja	Putalibazar	WUSC orientation with GESI	1/1/2018	1/1/2018	1	13	0	0	1	15	7	8
477	Syangja	Putalibazar	Financial & store management	2/1/2018	2/1/2018	1	13	0	0	1	15	7	8
478	Syangja	Putalibazar	Procurement of materials	3/1/2018	3/1/2018	1	13	0	0	1	15	7	8
479	Syangja	Putalibazar	Orientation on O&M and WSP++	4/1/2018	4/1/2018	1	13	0	0	1	15	7	8
480	Syangja	Putalibazar	Community Action Plan	5/1/2018	5/1/2018	1	13	0	0	1	15	7	8
481	Tanahun	Bhanu	Handwashing Day	15-10-17	15-10-17	13	7	0	0	20	40	23	17
482	Tanahun	Bhanu	GP/NP, Scheme level Post-Construction workshop	16-10-17	16-10-17	51	2	0	0	0	53	27	26
483	Tanahun	Bhanu	Handwashing Day	15-10-17	15-10-17	35	0	0	0	0	35	22	13
484	Tanahun	Bhanu	World toilet day	19-11-17	19-11-17	8	11	0	0	8	27	16	11
485	Tanahun	Bhanu	WSP++ Training and Preparation	29-11-17	1/12/2017	8	5	0	0	1	14	14	0
486	Tanahun	Bhanu	WUSC orientation with GESI	28-11-17	28-11-17	7	13	0	0	3	23	13	10
487	Tanahun	Bhanu	Procurement of materials	29-11-17	29-11-17	2	13	0	0	3	18	10	8
488	Tanahun	Bhanu	Financial & store management	30-11-17	30-11-17	2	13	0	0	3	18	10	8
489	Tanahun	Bhanu	Orientation on O&M and WSP++	1/12/2017	1/12/2017	2	13	0	0	3	18	10	8
490	Tanahun	Bhanu	Community Action Plan	2/12/2017	2/12/2017	2	13	0	0	3	18	10	8
491	Tanahun	Bhanu		1/11/2017	1/11/2017	1	9	0	0	33	43	9	34
492	Tanahun	Bhanu		22-12-17	22-12-17	2	13	0	0	39	54	15	39
493	Tanahun	Bhanu	Orientation on O&M and WSP++	2/1/2018	4/1/2018	8	14	0	0	4	26	13	13
494	Tanahun	Bhanu	Post-ODF/Total Sanitation orientation	20-12-17	20-12-17	1	22	0	4	15	42	14	28
495	Tanahun	Bhanu	Post-ODF/Total Sanitation orientation	8/1/2018	8/1/2018	6	17	0	0	22	45	21	24
496	Tanahun	Bhimad	Other, define	15-10-17	15-10-17	6	34	0	0	31	71	30	41
497	Tanahun	Bhimad	Other, define	15-10-17	15-10-17	4	17	0	0	19	40	15	25
498	Tanahun	Bhimad	Other, define	13-11-17	13-11-17	15	24	0	0	39	78	25	53

Annex 3 Capacity building events FY2074/075

SN	District	Municipality	Event Name	Starting Date	Ending Date	Dalit Total	Adibasi Janajati Total	Disadvantaged Terai Caste Total	Religious Minority Total	Other Total	All Total	Total Female	Total Male
499	Tanahun	Bhimad	Handwashing Day	15-10-17	15-10-17	2	14	0	0	11	27	15	12
500	Tanahun	Bhimad	World Toilet Day	19-11-17	19-11-17	32	140	0	0	50	222	124	98
501	Tanahun	Bhimad	Other, define	26-12-17	26-12-17	1	9	0	0	5	15	7	8
502	Tanahun	Bhimad	Other, define	27-12-17	27-12-17	33	17	0	0	0	50	22	28
503	Tanahun	Bhimad	Other, define	29-12-17	29-12-17	7	55	0	0	22	84	35	49
504	Tanahun	Bhimad	Other, define	8/1/2018	8/1/2018	2	36	0	0	0	38	26	12
505	Tanahun	Bhimad	Other, define	3/1/2018	3/1/2018	0	11	0	0	12	23	14	9
506	Tanahun	Bhimad	Other, define	4/1/2018	4/1/2018	1	9	0	0	9	19	7	12
507	Tanahun	Bhimad	Other, define	11/1/2018	11/1/2018	2	40	0	0	5	47	18	29
508	Tanahun	Bhimad	Other, define	12/1/2018	12/1/2018	6	28	0	0	35	69	34	35
509	Tanahun	Ghiring	Handwashing Day	15-09-17	15-09-17	19	31	0	0	2	52	44	8
510	Tanahun	Ghiring	WUSC orientation with GESI	27-10-17	27-10-17	6	11	0	0	0	17	8	9
511	Tanahun	Ghiring	Financial & store management	28-10-17	28-10-17	6	11	0	0	0	17	8	9
512	Tanahun	Ghiring	Procurement of materials	29-10-17	29-10-17	6	11	0	0	0	17	8	9
513	Tanahun	Ghiring	Orientation on O&M and WSP++	30-10-17	30-10-17	6	11	0	0	0	17	8	9
514	Tanahun	Ghiring	Community Action Plan	31-10-17	31-10-17	6	11	0	0	0	17	8	9
515	Tanahun	Ghiring	World Toilet Day	19-11-17	19-11-17	22	31	0	0	0	53	27	26
516	Tanahun	Ghiring	WSP++ Training and Preparation	1/7/2018	1/9/2018	0	9	0	0	0	9	5	4
517	Tanahun	Rishing	Handwashing Day	15-10-17	15-10-17	5	32	0	0	3	40	23	17
518	Tanahun	Rishing	World Toilet Day	19-11-17	19-11-17	0	175	0	0	0	175	99	76
519	Tanahun	Rishing	WUSC orientation with GESI	20-11-17	20-11-17	0	15	0	0	0	15	10	5
520	Tanahun	Rishing	Financial & store management	21-11-17	22-11-17	0	15	0	0	0	15	10	5
521	Tanahun	Rishing	Community Action Plan	23-11-17	24-11-17	0	15	0	0	0	15	10	5
522	Tanahun	Rishing	WSP++ Training and Preparation	1/1/2018	3/1/2018	0	17	0	0	3	20	7	13
523	Tanahun	Rishing	WSP++ Training and Preparation	4/1/2018	6/1/2018	0	10	0	0	0	10	5	5
524	Tanahun	Rishing	WSP++ Training and Preparation	5/1/2018	7/1/2018	0	10	0	0	0	10	4	6
TOTAL						**3,516**	**7,608**	**1,535**	**357**	**5,311**	**18,318**	**8,944**	**9,391**
%						**19%**	**42%**	**8%**	**2%**	**29%**		**49%**	**51%**
